




**UTTAR PRADESH CORE ROAD NETWORK DEVELOPMENT PROJECT**  
**PROJECT MANAGEMENT CONSULTANCY SERVICES FOR UTTAR PRADESH CORE**  
**ROAD NETWORK DEVELOPMENT PROGRAMME**

**Construction and Up-gradation of Four Packages of UPCRNDP Phase-I Roads and Design**  
**Project Report (DPR) for Phase II Roads in the State of Uttar Pradesh**  
**(1 NCB Package on Item Rate and 3 ICB Packages on EPC)**

**MONTHLY PROGRESS (O&M Period) REPORT No. 38**  
**AUGUST-2022**

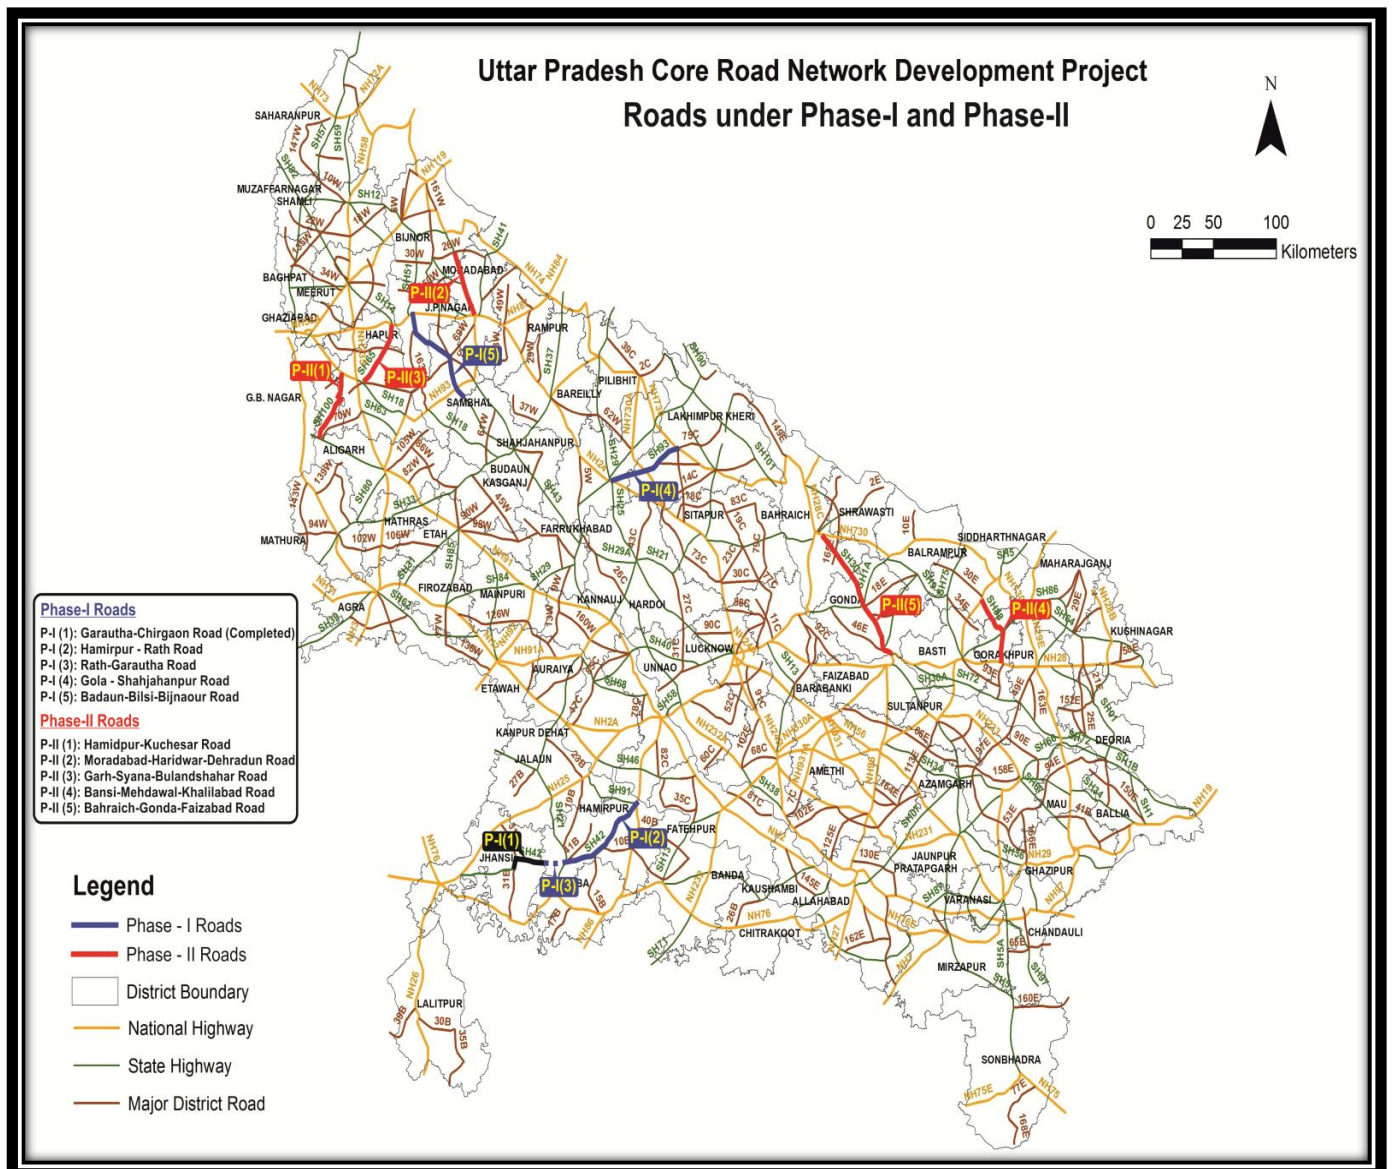

## **TABLE OF CONTENTS**

<b>INTRODUCTION .....</b>	<b>5</b>
<b>1 PROJECT BACKGROUND .....</b>	<b>5</b>
<b>2 PROJECT OVERVIEW .....</b>	<b>5</b>
<b>COMPONENT PART– A .....</b>	<b>6</b>
<b>3 PART- A .....</b>	<b>7</b>
3.1 PHASE-I ROADS .....	7
3.2 PHASE II ROADS .....	8
<b>4. PROJECT MANAGEMENT INFORMATION SYSTEM (PMIS) .....</b>	<b>12</b>
<b>5. FINANCIAL PROGRESS OF CONSULTANT (PART-B) .....</b>	<b>13</b>
<b>COMPONENT PART–B.....</b>	<b>14</b>
<b>6. INTRODUCTION .....</b>	<b>14</b>
<b>7. AWARDED PACKAGES.....</b>	<b>14</b>
<b>8. CONSTRUCTION/O&amp;M PERIOD AND MILESTONES.....</b>	<b>15</b>
<b>9. DESCRIPTION OF WORKS.....</b>	<b>15</b>
<b>10. DESIGN &amp; DRAWINGS OF EPC PACKAGES .....</b>	<b>16</b>
<b>11. HIGHWAY DETAILS .....</b>	<b>16</b>
<b>12. STRUCTURE DETAILS:.....</b>	<b>17</b>
<b>13. FINANCIAL PROGRESS .....</b>	<b>18</b>
<b>14. MEETING AND VISIT DURING THE REPORTING MONTH (PART-B) .....</b>	<b>18</b>
A. MEETING/TRAINING HELD DURING THE MONTH.....	18
B. SITE VISITS CARRIED OUT DURING THE MONTH .....	19
<b>15. CORRESPONDENCE MANAGEMENT .....</b>	<b>19</b>
<b>16. CONSTRUCTION SUPERVISION CONSULTANT’S MOBILIZATION .....</b>	<b>20</b>
A. ORGANIZATION.....	20
B. CONSULTANT’S MOBILIZATION .....	21
i. Staff.....	21
ii. Vehicles.....	22
iii. Offices.....	22
<b>CONTRACT PROJECT ACTIVITIES.....</b>	<b>23</b>
<b>17. CONSTRUCTION PACKAGE –UPG-02 .....</b>	<b>23</b>
A. INTRODUCTION .....	23
B. SALIENT FEATURES OF CONTRACT .....	24
<b>18. WORK PROGRESS .....</b>	<b>25</b>
i. Design and Drawings .....	25

ii.	Maintenance Work Programme .....	25
iii.	Monthly Maintenance Payment Certificate .....	25
iv.	Physical Progress .....	25
v.	Quality Control/Quality Assurance .....	25
vi.	Meetings & Site Inspections.....	25
vii.	Key Issues .....	25
viii.	Weather.....	26
<b>19.</b>	<b>CONTRACT PACKAGE UPG-01 .....</b>	<b>27</b>
A.	INTRODUCTION .....	27
B.	DESCRIPTION OF WORKS .....	28
C.	CONSULTANT MOBILIZATION .....	28
D.	CONSTRUCTION ACTIVITIES: FOCUSES ON O&M WORKS .....	28
i.	Mobilization of Contractor .....	28
E.	WORK PROGRESS .....	29
i.	Design and Drawings .....	29
ii.	Project Completion /Operation and Maintenance .....	29
iii.	Maintenance Work Programme .....	29
iv.	Monthly Maintenance Statement (MMS) .....	29
v.	Physical Progress .....	29
F.	QUALITY CONTROL / QUALITY ASSURANCE.....	29
G.	MEETINGS & SITE INSPECTIONS .....	29
H.	KEY ISSUES .....	30
I.	WEATHER .....	30
<b>20.</b>	<b>CONTRACT PACKAGE UPG-03 .....</b>	<b>31</b>
A.	INTRODUCTION .....	31
B.	SALIENT FEATURES .....	31
C.	DESCRIPTION OF WORKS .....	32
D.	CONSULTANT MOBILIZATION .....	32
E.	STAFF MOBILIZATION.....	32
F.	CONSTRUCTION ACTIVITIES: FOCUSES ON O&M WORKS .....	32
i.	Mobilization of Contractor .....	32
G.	WORK PROGRESS .....	33
i.	Design and Drawing.....	33
ii.	Maintenance Work Programme .....	33
iii.	Financial Progress .....	33
iv.	Monthly Maintenance Statement (MMS) .....	33
v.	Physical Progress .....	33
H.	MEETINGS & SITE INSPECTIONS .....	34
I.	KEY AND POTENTIAL ISSUES .....	34
J.	WEATHER REPORT .....	34
<b>21.</b>	<b>CONTRACT PACKAGE UPG-04 .....</b>	<b>35</b>
A.	INTRODUCTION .....	35
B.	SALIENT FEATURES .....	35
C.	DESCRIPTION OF WORKS .....	36
D.	MOBILIZATION OF CONSULTANT .....	36
E.	STAFF MOBILISATION .....	36
F.	CONSTRUCTION ACTIVITIES: FOCUSES ON O&M WORKS .....	36
G.	WORK PROGRESS .....	37

i.	<i>Design and Drawings</i> .....	37
ii.	<i>Financial Progress</i> .....	37
iii.	<i>Monthly Maintenance Statement (MMS)</i> .....	37
iv.	<i>Physical Progress</i> .....	37
v.	<i>Quality Control / Quality Assurance</i> .....	37
H.	MEETINGS & SITE INSPECTIONS .....	37
I.	KEY ISSUES .....	38
J.	WEATHER .....	38

**ENVIRONMENT, SOCIAL, HEALTH AND SAFETY ..... 39**

**22. ENVIRONMENT, SOCIAL, HEALTH AND SAFETY ..... 40**

A.	INTRODUCTION .....	40
B.	ESHS ISSUES AND CORRECTIVE ACTIONS TAKEN .....	40
i.	<i>Essential Project Insurances</i> .....	40
ii.	<i>Borrow Areas</i> .....	41
iii.	<i>Status of O&amp;M Phase ESMP Issues along with updated status is as below:</i> .....	42
C.	OPERATION AND MAINTENANCE STAGE MONITORING .....	44
D.	CONSTRUCTION SITE MANAGEMENT .....	45
i.	<i>Compliance Status of Environmental Safeguard</i> .....	45

**23. CONSTRUCTION SAFETY MONITORING AND COMPLIANCE REPORT ..... 46**

A.	ROAD SAFETY PROJECT IMPLEMENTATION STATUS .....	47
B.	SAFETY EQUIPMENT AT SITES DURING O&M PERIOD .....	50
C.	RECORD WITH DATES OF COMPLETED ROAD SAFETY AUDITS ON PHASE-I ROADS .....	50

**24. SOCIAL MONITORING AND COMPLIANCE REPORT ..... 51**

**INTRODUCTION ..... 51**

**RESETTLEMENT ACTION PLAN (RAP) IMPLEMENTATION BY NGO ..... 52**

**STATUS OF CPRS ..... 52**

**COMPONENT PART- C ..... 53**

**25. PART-C COMPONENT ..... 54**

A.	OVERALL PROGRESS OF UPCRNDP – PMC’S SCOPE.....	54
B.	STATUS OF CONSULTANCY SERVICES REQUIRED AND MOBILIZED UNDER UPCRNDP .....	58
C.	STATUS OF VARIOUS CIVIL WORKS (PROCUREMENT STATUS OF PHASE-II ROADS).....	60
D.	FINANCIAL PROGRESS OF CONSULTANT (PART-C).....	62

**PHOTOGRAPHS (UPG-01/UPG-02/UPG-03/UPG-04)**

**APPENDIX A UPG-01 (ANNEXURE-A TO ANNEXURE-E)**

**APPENDIX B UPG-02 (ANNEXURE-A TO ANNEXURE-E)**

**APPENDIX C UPG-03 (ANNEXURE-A TO ANNEXURE-E)**

**APPENDIX D UPG-04 (ANNEXURE- A TO ANNEXURE-E)**

## **INTRODUCTION**

### **1 Project Background**

Uttar Pradesh has a road network of 299,604 Km, out of which 174,451 Km is under Public Works Department (PWD). The roads under PWD comprise 7,550 Km of National Highways (NHs), 7530 Km of State Highways (SHs) 5,761 Km of Major District Roads (MDRs), 3254 Km of Other District Roads (ODRs) and 138,702 Km of Village Roads (VRs). Only about 60% of SHs are two-lane (7 m). In the entire state 62% of MDRs and 83% of ODRs have widths less than 7m.

With a view to improve the Transport Network System, UPPWD has identified 24,095 Km of Core Road Network for the development. This network comprises of NH, SH, MDR, ODR and the details are presented in the table below:

<b>Road Category</b>	<b>Length (Km)</b>
National Highway (NH)	7,550
State Highway (SH)	7,530
Major District Road (MDR)	5,761
Other District Road (ODR)	3,254
<b>Total</b>	<b>24,095</b>

### **2 Project Overview**

The Civil Works component has been taken in two Phases. The Terms of Reference (TOR) for consultancy contract identifies roads with an aggregate length of 419 Km as Phase-I and remaining roads to be undertaken under Phase- II. The total budgeted Project Cost is about INR 3,500 Crore, out of which funds available for the works has been estimated at about INR 3,000 Crore.

Public Works Department (PWD) on behalf of Government of Uttar Pradesh engaged M/s Egis India Consulting Engineers Pvt. Ltd. to carry out Consultancy Services for Uttar Pradesh Core Road Network Development Plan. The Consultant is required to provide all required assistance and support to the PWD /GoUP/ Bank Task Team in complying with World Bank Investment Project Financing Policies and Procedures.

The Project Management Consultancy services will be undertaken in three Parts.

**PART A:** Project Preparation including Detailed Engineering Design and Contract Documentation (Lump Sum) 24 months from commencement of services.

**PART B:** Construction Supervision of Phase I Civil Works (Time Based) Until completion of Civil Works of Phase-I roads including DLP & Maintenance (24-30 months + 60 months Maintenances period including DLP)

**PART C:** Project Management Services (Time Based) Initially for 5 years further extension based on Consultants performance.

The Contract was signed on 8<sup>th</sup> August 2014 and it was agreed that the start date for the assignment shall be considered as 19<sup>th</sup> August 2014. The initial discussions were held on 14<sup>th</sup> August 2014 with Client on the priority roads and scheduled deliverables. Accordingly, the teams were mobilized and activities commenced on Proposed Phase-I roads.

This **Monthly Report No. 38** is prepared and submitted with respect to Terms of Reference (TOR) for Consultancy Services to Agreement between the Chief Engineer (EAP), Uttar Pradesh Public Works Department (UPPWD) and Egis India Consulting Engineers Pvt. Ltd, New Delhi.

**COMPONENT PART– A**

PROJECT PREPARATION INCLUDING DETAILED ENGINEERING DESIGN  
AND CONTRACT DOCUMENTATION

### 3 PART- A

#### 3.1 Phase-I Roads

Roads considered under Phase-I for Part-A Component of PMC Services as per contract have been modified as under:

S. No.	Phase-I Road/Works as per Contract			Subsequent Revision in Roads/Works by the Client		Present Status
	Road Name	Category	Length (Km)	Revised	Design Length	
1	Hamirpur-Rath-Gursahayganj-Jhansi Road	SH-42	168	Splits into three packages	158.812	Except Missing Link – Civil works on 2 Contract package is completed.
2	Gola-Shahjahanpur Road	SH-93	59	No Change	57.535	Under Maintenance
3	Badaun-Bilsi-Bijnaour	SH-51	79	No Change	79.125	Under Maintenance
4	Utraula-Faizabad Road*	SH-9	59	Replaced by Balrampur – Utraula-Faizabad Road	87.150	Client has further excluded from WB funding.
5	Lepulekh-Bhind(From Jalalabad) Road	SH-29	54	Omitted: Taken as NH	0	Deleted
6	Bridge Over River Sharda	–	–	Shifted to Phase-II	–	Relinquished due to Land acquisition constraints.
		<b>Total</b>	<b>419</b>		<b>382.622</b>	

**Note:** \*Proposed Roads at sl.no.4 has been added 28Km of length as “Balrampur-Utraula-Faizabad Section” of SH-26 and SH-9 for the DPR works.

The Roads finalized under Phase-I are as under:

S. No.	Package	Road/Works	Category	Length (Km)	Civil Cost (INR Cr)	Present Status
1	UPG-01	Hamirpur-Rath	SH-42	72.785	262.40	Under O&M from 12 <sup>th</sup> July 2021
2	UPG-02	Garautha-Chirgaon	SH-42	49.145	189.99	Under O&M from 1 <sup>st</sup> November 2020
3	UPG-03	Gola-Shahjahanpur	SH-93	56.388	356.90	Under O&M from 15 <sup>th</sup> March 2022
4	UPG-04	Badaun-Bilsi-Bijnaour	SH-51	79.125	334.00	Under O&M from 10 <sup>th</sup> January 2022

The detailed project report of Phase-I Roads is given under Part-B Component.

SH-42 Missing Link Section Rath – Garautha (Approx.35.882Km) –2 Lane (Cost 251 INR Cr.)

- Bidding Document submitted on 20<sup>th</sup> February 2021
- Bidding documents of Missing Link approved by UPPWD & World Bank
- Bid was floated on 7<sup>th</sup> January, 2022, only one bid was received hence cancelled following Government Procurement Policy i.e. a minimum 3 responsive bidders required for opening of bids.
- Therefore Bid was refloated on 31<sup>st</sup> May, 2022; 3 bids received and all qualified after evaluating the Technical Part of the Bids.
- Technical Bid Evaluation Report sent to WB on 30.06.2022 for approval.
- Micro Plan of Missing Link submitted to UPPWD vide Egis letter No. Egis India/LKO/UPCRNDP/2022/1921 Dated 26.08.2022.
- Forest Proposal of Missing Link submitted to UPPWD vide Egis letter No. Egis India/LKO/UPCRNDP/2022/1920 Dated 26.08.2022.

### 3.2 Phase II Roads

Client (EAP-PWD) vide letter No.2018/1-02/UPCRNDP/CEWB/2019 Dated 16/10/2019 granted Five Roads with G.O.No. 1480/23-12-2019-88/15 (R) Dated 09/10/2019 for Detailed Project Report Preparation.

List of selected roads to be designed and constructed under Phase-II are as under:

Sl.No	Phase – II Road/Works as approved by State Govt.				DPR Study Revealed	
	Name of Road/work	Category	Length	Estimated Cost (INR Cr.)	Revised Length (km)	Revised Estimated Cost INR(Cr)
1	Moradabad-Haridwar-Dehradun Road	SH-49	36.000	356.40	36.170	444.95
2	Garh- Syana-Bulandshahar Road	SH-65	49.500	499.20	49.674	700.74
3	Baharaich - Gonda-Faizabad Road	SH-30	60.100	365.00	59.237	437.74
4	Hamidpur- Kuchesar Road	SH-100	47.500	289.20	19.109	155.75
5	Bansi-Mehndawal-Khalilabad Road	SH-88	32.000	193.10	28.870	257.06
<b>Total</b>			<b>225.1</b>	<b>1702.9</b>	<b>193.060</b>	<b>1996.26</b>

#### Phase-II Roads Progress

The Status of DPR of roads under Phase-II is given in following tables:

S. No.	Proposed Phase-II Roads				DPR Documents - Approval Status (By World Bank & PWD)				
	Roads	Category	Length (Km)	Total Project Cost (INR Cr.)	Proposed Lane	DPR (Detailed Engineering)	EIA/EMP	RAP (Social)	Bid Document
1	Rath – Garautha Road (Missing Link)	SH-42	35.882	277.75	2 Lane	Approved	Approved	Approved	Approved

2	Bansi-Mehdawal-Khalilabad	SH-88	28.870	257.06	2 Lane	Approved	Approved	Approved	Approved
3	Bahraich-Gonda-Faizabad	SH-30	59.237	437.74	2 Lane	Approved	Approved	Approved	Approved
4	Garh-Siyana-Bulandshahr Road	SH-65	49.674	700.74	4 Lane	Submitted	Submitted	Submitted	Submitted
5	Moradabad-Haridwar-Dehradun	SH-49	36.170	444.95	4 Lane	Approved	Approved	Approved	To be submitted
6	Hamidpur-Kuchesar Road	SH-100	19.100	155.75	2 Lane	Submitted	Submitted	Submitted	Submitted
<b>TOTAL</b>			<b>193.051</b>	<b>2273.99</b>					
<b>Note:</b>	The Bid Documents for SH-49 road shall be prepared with similar provisions of Bid Document for SH-30 as these Bids will also be ICB expected to be submitted by end of 5 <sup>th</sup> September 2022.								

### Phase-II Roads - Forest Clearance

The Status of progress of Pre-bid activities for Environmental Safeguard and Forest/  
Environmental Clearance / Tree Cutting for roads under Phase-II is given in following tables:

Sl. No.	Proposed Phase-II Roads		FC/EC - Application and Approval Status (by MoEFCC)						
	Roads	Length (Km)	FC/EC	FC No.	PF Area (Ha)	RF Area (Ha)	Non-Forest (Ha)	Trees in PROW/ To be Cut	Remarks
1	Rath – Garautha Road (Missing Link) SH-42	35.882	FC Applicable	FP/UP/ROAD/ 117342/ 2020	1.0684	17.117	88.8566	2454	Revised FC Proposal submitted on 29-08-2022; Demand for payment is awaited
2	Bansi-Mehdawal-Khalilabad SH-88	28.870	Not Applicable	NA	0	0.000	4.8782	10880	Demand received; Payment to be made
3	Bahraich-Gonda-Faizabad SH-30	59.237	FC Applicable	FP/UP/ROAD/ 147236/2021	82.7212	0.00	0.511	6204/ 29030	Demand for payment is awaited
4	Garh-Siyana-Bulandshahr Road SH-65	49.674	EC Applicable	To be Applied	26.984	0.000	34.474	11660/ 6995	Under Process
5	Moradabad-Haridwar-Dehradun SH-49	36.170	FC Applicable	FP/UP/ROAD/1 53873/2022	35.624	0.000	12.895	7176	EDS raised on 31-08-2022- for correction in uploaded KML File;
6	Hamidpur-Kuchesar Road SH-100	19.100	Not Applicable	NA	0	0.000	3.866	9630	Demand Payment done by PWD
<b>TOTAL</b>		<b>228.933</b>			<b>146.3976</b>	<b>17.117</b>	<b>145.4808</b>	<b>38212/ 36025</b>	
<b>Note:</b>	FC is not involved for SH-88 & SH-100, however to cut the affected trees Demand for payment is completed for both the roads. Such as for SH-100 Hamirpur-Kuchesar Road (FD, Gautam Budhha Nagar INR 60.73 Lac; FD, Bulandshahr INR 608.53 Lac) and for SH-88 (Bansi-Mendhwal-Khalilabad Road (FD-Siddhartha Nagar INR 267.27; FD-Sant Kabir Nagar INR 69.36).								

**Phase-II Roads – Status of Social Safe Guard**
**1. Submission and Approval of RAP/SMP**

Sr. No.	Phase-II Roads	Submitted to IER by EGIS	Comments Received from IER	Revised Report to IER	IER Clearance	Approval of UP PWD	Approval of the World Bank
1.	Bahraich-Gonda-Faizabad Road (SH-30)	09.03.2021	03.05.2021	25.06.2021	22.07.2021	30.07.2021	09.08.2021
2.	Bansi-Menhdawal-Khalilabad Road (SH-88)	09.03.2021	03.05.2021	25.06.2021	12.07.2021	30.07.2021	09.08.2021
3.	Rath- Garautha Road (Missing Link) (SH-42)	13.05.2021	27.05.2021	07.07.2021	22.07.2021	30.07.2021	09.08.2021
4.	Moradabad-Haridwar-Dehradun Road (SH-49)	09.03.2021	03.05.2021	13.07.2021	22.07.2021	30.07.2021	08.02.2022
5.	Garh-Siyana-Bulandshahr Road (SH-65)	24.05.2021	31.05.2021	18.07.2021	22.07.2021	30.07.2021	08.02.2022
6.	Hamidpur-Kuchesar Road (SH-100)	07.06.2021	22.07.2021	09.08.2021	17.08.2021	30.08.2021	08.02.2022

**2. Status of Pre Activities**

Sr. No.	Road No	District	Tehsil	No. of Villages affected	Land to be acquired (Ha)	No. of TH	Verification affected land	Submission of verified report by Rev Dept to PWD	Signing of Sahmati Patra from THs	Date of meeting of district to Committee on land proposal	Approval of land acquisition proposal from Committee	Remarks
1	SH 42	Hamirpur	Rath	13	67.453	874	Completed	Received	Completed	04.07.2022 & 30.08.2022	Awaited	81.4 percent consent (Sahmati Patra) has been obtained from titleholders in total affected 13 villages. (As per the GoUP order ,2015 for acquisition of land through direct purchase , overall 80 % Sahmati (consent) is mandatory
2		Jhansi	Gharauth	4	39.589	392	Completed	Received	Completed	22.06.2022	12.07.2022	Registration of affected land started
3	SH 88	Siddhart h Nagar	Bansi	12	1.887	317	Completed	Received	In progress			Preparation of land proposal is in progress
4		Sant Kabir Nagarr	Menhdawal	9	2.912	378	Completed	Received	Completed			Preparation of land proposal is in progress
5	SH 30	Bahraich	Bahraich	3	0.209	63	Completed					
6		Gonda	Gonda	2	0.302	18	Completed	Completed	Completed	Yet to be decided		
7	SH 49	Moradabad	Moradabad / Kanth	18	11.011	866	In progress					
8	SH 65	Bulandshahr	Bulandshahr	26	28.647	828	In progress					
9		Hapur	Garhmukteswar	8	4.106	355	In progress					
10	SH 100	Bulandshahr	Sikandrabad	8	3.866	323	In progress					
<b>Total</b>				<b>103</b>	<b>159.98</b>	<b>4414</b>						

**Phase-II Roads Meetings**

**06.08.2022**- Meeting was organized under the Chairmanship of Engineer-In-Chief to review the works of Road Safety, Road Asset Management, Environmental/Forest Clearances and EIA Status under Phase-II Roads (SH-30, SH-49 & SH-65) and Stage-II Clearance under the Phase-I Road (UPG-03) and Minutes of Meeting (MoM) issued by the Engineer-In-Chief vide letter No. 1778/Meeting/CEEAP/2022 Dated 11.08.2022 forwarded by the UPPWD vide letter No. 1813/1-12/UPCRNDP/CEEAP/2022 Dated 22.08.2022.

**08.08.2022**- Meeting was organized by the SE,PWD,Kanpur on 08.08.2022 at PWD Inspection House, Hamirpur to Review the Progress of Land Acquisition and Forest Proposals of Missing Link (Rath-Garautha), SH-42 and the same was attended by the PWD Officials, Team Leader of Sugam International Sansthan (NGO) and Egis Environmental Specialist Mr. Dev Brat Singh. Minutes of Meeting (MoM) issued by the Authority vide letter No. 734-16 C (i)-WBPCCK/2022 Dated 11.08.2022.

**08.08.2022**- Assistant Social Development Specialist Mr. Bikram Singh along with UPPWD Social Expert attended Meeting with ADM, Hamirpur regarding land acquisition proposal of Missing Link Project Road.

**20.08.2022**- Meeting was organized by the SE,PWD,Kanpur on 20.08.2022 at Office of Superintending Engineer Office,World Bank Project Circle, Kanpur to Review the Progress of preconstruction activities of Missing Link (Rath-Garautha), SH-42 and the same was attended by the PWD Officials and Mr. Saini from Sugam International Sansthan (NGO). Minutes of Meeting (MoM) issued by the Authority vide letter No. 745/8C-WBPCCK/2022 Dated 22.08.2022.

**25.08.2022**- Meeting regarding land acquisition proposal of Gonda-Bahraich-Faizabad (SH-30) Road attended by the Assistant Social Development Specialist Mr. Bikram Singh along with the UPPWD officials and Team Leader of Sugam International Sansthan (NGO) at ADM Office, Gonda.

**26.08.2022**- Meeting attended by the Assistant Social Development Specialist Mr. Bikram Singh and Mr. Dev Brat Singh at UPPWD World Bank Division, Kanpur regarding finalization of micro plan and ID cards of Title Holders and regarding Forest Proposal of Missing Link respectively.

**29.08.2022**- Meeting was organized under the Chairmanship of Chief Engineer(EAP) at UPPWD Office to Review the Progress of preconstruction activities of Missing Link (Rath-Garautha), SH-42, Phase-II Roads & Stage-II Clearance of Phase-I Roads and the same was attended by the PWD Officials and Deputy Team Leader Mr. Sarwan Singh Saini. Minutes of Meeting (MoM) issued by the Authority vide letter No. 1878/Meeting/CEEAP/2022 Dated 30.08.2022.

**29.08.2022**- Meeting attended by the Assistant Social Development Specialist Mr. Bikram Singh along with UPPWD officials and Team Leader Sugam International Sansthan (NGO) at DM Office, Siddhartha Nagar regarding land acquisition activities of Bansi-Menhdawal-Khalilabad Road (SH-88).

## **Phase-II Roads Site Visits Carried out during the Month**

**03.08.2022 to 10.08.2022** – Assistant Social Development Specialist Mr. Bikram Singh visited Missing Link Project Road (Rath) along with UPPWD Social Expert for assisting NGO in preparation of micro plan (Title Holders), payment sheet for registry, review and verification of micro plan of Tahsil Garautha. Micro Plan reviewed and recommended to the Authority vide Egis letter No. Egis India/LKO/UPCRNDP/2022/1921 Dated 26.08.2022.

**29.08.2022 to 31.08.2022** - Joint verification of affected land of Bansi-Menhdawal-Khalilabad Road (SH-88) was carried out by the Asst. Social Development Specialist Mr. Bikram Singh along with UPPWD officials, Sugam International Sansthan (NGO) Team and Revenue Department details of which are as follows:

**Tahsil Bansi District Siddhartha Nagar** – Joint verification of affected land in total 12 villages completed with concerned revenue officials and Sugam International Sansthan (NGO). Therefore, Original Verified Reports have been received from SDM Office, Bansi vide letter No. 220/AA.Lee./2022-23 Dated 01.09.2022 which are with NGO Team Leader.

**Tahsil Menhdawal District Sant Kabir Nagar** – Re-verification of affected land in total 3 villages completed with concerned revenue officials and Sugam International Sansthan (NGO). Therefore, Original Verified Reports of all Nine Villages have been received from SDM Office, Menhdawal vide letter No. 403/S.T.-22 Dated 03.09.2022 which are with NGO Team Leader.

## **4. Project Management Information System (PMIS)**

The Progress on various modules of PMIS is indicated below:

Sl. No.	Modules	Status
1	Grievance Redressal System	Completed
2	Project Website	Completed
3	Content Management System (CMS) / Document Management System	Completed
4	Knowledge And Documentation Centre	Completed
5	Works Estimation System / BOQ automation, Measurement System, Risk Management, Quality Management System	Completed
6	Financial Accounting & Cost Management System	Completed
7	E-Procurement System (provide interface)	Completed
8	Scope Management System	Completed
9	Monitoring and evaluation (M&E) & Decision Support System	Completed
10	Computer Aided Design (CAD) System	Completed
11	Project Roads Database	Completed

Note: Construction Supervision Manual, Road Maintenance Manual and Quality Management Program all reports of Phase-II Roads were submitted on 18<sup>th</sup> November 2021.

## 5. Financial Progress of Consultant (PART-B)

Financial Expenditure of PMC Services up to August-2022

PART-B Up to August 2022 (INR) - CLAIMED AMOUNT

Sl No.	Description	Contract Amount (INR)	Amt as per Variation (VO-1) (INR)	Cumulative up to Current Invoice (INR)	Balance (INR) w.r.t. VO-1
1	Remuneration for Key Professionals	8,22,86,700	9,03,54,046	6,39,94,389	2,63,59,657
2	Remuneration for Non-Key Professionals	18,79,38,800	14,74,53,510	8,50,72,120	6,23,81,390
3	Reimbursable Expenses	4,46,07,516	4,83,63,117	2,93,03,258	1,90,59,859
<b>Total</b>		<b>31,48,33,016</b>	<b>28,61,70,673</b>	<b>17,83,69,767</b>	<b>10,78,00,906</b>
4	Escalation			4,33,10,584	
<b>Grand Total</b>		<b>31,48,33,016</b>	<b>28,61,70,673</b>	<b>22,16,80,351</b>	

## **COMPONENT PART-B**

### **CONSTRUCTION SUPERVISION OF CIVIL WORKS**

#### **6. Introduction**

Civil Works Component under Part-B concedes for providing Construction Supervision Services and Contract Administration for the Improvement of Uttar Pradesh Core Road Network Development Project.

#### **7. Awarded Packages**

<b>Sl. No.</b>	<b>Package Name</b>	<b>Contract Name</b>	<b>Contractor</b>	<b>Contract Amount (INR Cr.)</b>	<b>Length (Km)</b>	<b>Appointed Date</b>
1	Up-gradation and Maintenance of Garautha-Chirgaon Section of SH-42 from Km 118.600 to Km 167.745 (UPG-02)	NCB No. UPCRNDP/UPG/02/2014	M/s NKC Projects Pvt. Ltd.	189.99	49.145	15-01-2018
2	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Hamirpur-Rath Section of SH-42 from Km 2.065 to Km 74.255 (UPG-01)	ICB No. UPCRNDP/UPG/01/2018	M/s GHV (India) Pvt. Ltd.	262.39	72.785	25-06-2019
3	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Gola-Shahjahanpur Section of SH-93 from Km 1.280 to Km 58.580 (UPG-03)	ICB No. UPCRNDP/UPG/03/2018	M/s APCO Infratech Pvt. Ltd.	356.90	57.535	11-11-2019
4	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Badaun-Bilsi-Bijnaour Section of SH-51 from Km 58.400 to Km 137.820 (UPG-04)	ICB No. UPCRNDP/UPG/04/2018	M/s GAWAR Construction Ltd.	334.00	79.125	04-11-2019
	<b>TOTAL</b>			<b>1143.28</b>	<b>258.59</b>	

## 8. Construction/O&M Period and Milestones

Package Name	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Hamirpur-Rath section of SH-42 from Km 2.065 to Km 74.255 (UPG-01)	Up-gradation and Maintenance of Garautha-Chirgaon Section of SH-42 from Km 118.600 to Km 167.745 (UPG-02)	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Gola-Shahjahanpur section of SH-93 from Km 1.280 to Km 58.580 (UPG-03)	Engineering Procurement and Construction Contract for Up-gradation and Maintenance of Badaun-Bilsi-Bijnaour section of SH-51 from Km 58.400 to Km 137.820 (UPG-04)
Date of Agreement	19-06-19	05-01-17	26-06-19	05-07-19
Appointed Date	25-06-19	15-01-18	11-11-19	04-11-19
Construction Period	730 days	24 Months	730 days	730 days
Maintenance Period	1826 days	5 Years	1826 days	1826 days
Scheduled Completion Date	23-06-21	14-01-20	09-11-21	02-11-21
Extended Scheduled Completion Date	02-09-21	31-10-20	15-03-22	10-01-22
Provisional Completion Certificate	12-07-21	-	-	-
Actual Completion Date	12-08-21	31-10-20	15-03-22	10-01-22
Maintenance Period Start date	12-07-21	01-11-20	15-03-22	10-01-22
O&M Period including Defect Liability Period (DLP)	11-07-26	31-10-25	14-03-27	09-01-27
NOTE:	DLP for UPG-02 Item Rate Contract was only for one year which completed on 31 <sup>st</sup> December 2021 with the extended period of two months.			

## 9. Description of Works

The works of Phase-I contract packages were completed under Engineering and Procurement mode of Contract except for Package UPG-02 which was executed on Unit Rate (BOQ) contract. Contracts utilized both new and existing alignments. The work were involves improvement of State Highways including geometric improvements and realignments to standard 2-lane of 7 m carriageway, 1.5 m paved shoulders, and soft shoulders.

## 10. Design & Drawings of EPC Packages

The Status of As Built Drawings for Phase-I Roads are as below:

Name of Road/ Work	Contractor	Length (Km)	Status of As Built Drawings	
			Submitted by Contractor	Approved by PMC & Submitted to Authority
Hamirpur-Rath SH-42 (UPG-01)	M/s GHV (India) Pvt. Ltd.	72.785	12.02.2022	17.05.2022
Garautha-Chirgaon SH-42 (UPG-02)	M/s NKC Projects Pvt. Ltd.	49.145	29.12.2020	31.12.2020
Gola-Shahjahanpur SH-93 (UPG-03)	M/s APCO Infratech Pvt. Ltd.	57.535	Draft Copy of Structures and Plan & Profile Drawings reviewed by the AE and observations notified to the Contractor for incorporation. Also instructed to submit Highway Drawings for AE's review after checking by the Design Consultant. Resubmission Awaited.	-
Badaun-Bilsi- Bijnaour SH-51 (UPG-04)	M/s GAWAR Construction Ltd.	79.125	Submission Awaited	-

## 11. Highway Details

At present the civil construction works are completed on Phase-I Contract Packages. Project Highway taken-up for O&M Activities are presented in Table below:

Project Highway Road Section:								
Project Road	UPG-01: Hamirpur-Rath SH-42		UPG-02: Garautha- Chirgaon SH-42		UPG-03: Gola- Shahjahanpur SH- 93		UPG-04: Badaun- Bilsi-Bijnaour SH- 51	
Contractor	M/s GHV (India) Pvt. Ltd.		M/s NKC Projects Pvt. Ltd.		M/s APCO Infratech Pvt. Ltd.		M/s GAWAR Construction Ltd.	
Pavement	Length (in Km)		Length (in Km)		Length (in Km)		Length (in Km)	
Project Length	As per CA	Revised	As per CA	Revised	As per CA	Revised	As per CA	Revised
Flexible Pavement/Widening and Strengthening of Existing Road/new 2-lane realignment	55.85	55.136	49.145	49.145	57.535	56.388	79.125	79.125


Rigid Pavement: Reconstruction / New 2-lane realignment / bypass	16.935	16.935	0.000	0.000	0.000	0.000	0.000	0.000
<b>Total</b>	<b>72.785</b>	<b>72.071</b>	<b>49.145</b>	<b>49.145</b>	<b>57.535</b>	<b>56.388</b>	<b>79.125</b>	<b>79.125</b>
<b>Length for O&amp;M</b>	<b>72.071</b>		<b>49.145</b>		<b>56.388</b>		<b>78.309</b>	

Note: At four locations on Project Highway of UPG-04 Minor Bridge/Culvert construction across the road has been carried out by the Irrigation Department. Client through MOU has assigned the maintenance responsibility for affected 816 Rm length of completed project highway to the Concerned Agency (Irrigation Department).

## 12. Structure Details:

<b>Project Road - Completed Structures:</b>								
<b>Project Road</b>	<b>UPG-01: Hamirpur-Rath SH-42</b>		<b>UPG-02: Garautha- Chirgaon SH-42</b>		<b>UPG-03: Gola- Shahjahanpur SH-93</b>		<b>UPG-04: Badaun-Bilsi- Bijnaour SH-51</b>	
<b>Contractor</b>	<b>M/s GHV (India) Pvt. Ltd.</b>		<b>M/s NKC Projects Pvt. Ltd.</b>		<b>M/s APCO Infratech Pvt. Ltd.</b>		<b>M/s GAWAR Construction Ltd.</b>	
<b>Type of Structures (In Nos.)</b>	<b>As per CA</b>	<b>Revised</b>	<b>As per CA</b>	<b>Revised</b>	<b>As per CA</b>	<b>Revised</b>	<b>As per CA</b>	<b>Revised</b>
Major Bridges (Reconstruction)	0	0	0	0	1	1	0	0
Minor Bridges (Reconstruction)	1	4	5	5	4	4	2	2
Box Culverts (Reconstruction)	38	43	47	46	21	18	11	11
HP Culverts (Reconstruction)	34	36	25	29	17	17	69	69
Minor Bridge (Widening +Rep.)	3	0	1	1	3	3	1	1
Culverts (Widening +Rep.)	29	28	17	13	36	32	19	18
Repair of Structures	21	18	4	4	15	18	4	4
Wild Animal Under Pass	0	0	0	0	0	3		0
Slab Culverts (Reconstruction)	0	0	0	0	0	0	6	6
<b>Total</b>	<b>126</b>	<b>129</b>	<b>99</b>	<b>98</b>	<b>97</b>	<b>96</b>	<b>112</b>	<b>111</b>

### 13. Financial Progress

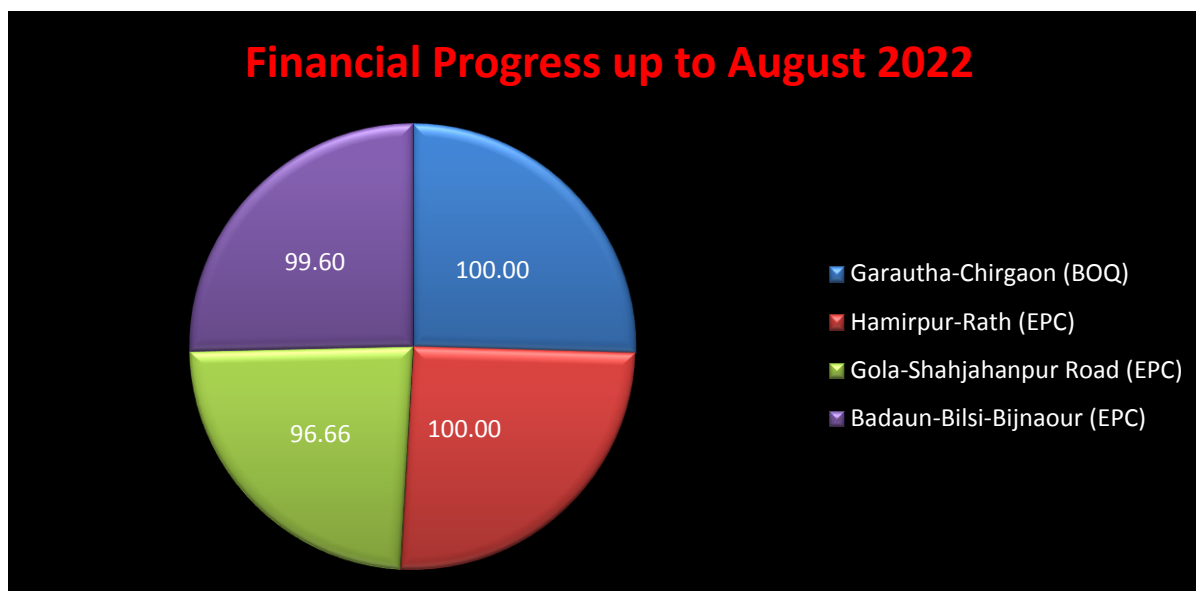

Package	Cost of Project (Cr.)	Certified IPC Amount (Cr.)	Paid IPC Nos.	Remarks
Garautha-Chirgaon (BOQ)(Revised Cost) Part-1	183.92	183.92	IPC-24	Excluding Maintenance (Statement at Completion)
Hamirpur-Rath (EPC) (Revised Cost)	275.65	275.65	IPC-18	Final IPC
Gola-Shahjahanpur Road (EPC)	356.9	345.01	IPC-16	
Badaun-Bilsi-Bijnaour (EPC)	334.08	332.76	IPC-18	
<b>TOTAL (In Crore)</b>	<b>1150.55</b>	<b>1113.92</b>		

### 14. Meeting and Visit during the Reporting Month (Part-B)

#### a. Meeting/Training held during the Month

**06.08.2022-** Meeting was organized under the Chairmanship of Engineer-In-Chief to review the works of Road Safety, Road Asset Management, Environmental/Forest Clearances and EIA Status under Phase-II Roads (SH-30, SH-49 & SH-65) and Stage-II Clearance under the Phase-I Road (UPG-03) and Minutes of Meeting (MoM) issued by the Engineer-In-Chief vide letter No. 1778/Meeting/CEEAP/2022 Dated 11.08.2022 forwarded by the UPPWD vide letter No. 1813/1-12/UPCRNDP/CEEAP/2022 Dated 22.08.2022.

**29.08.2022-** Meeting was organized under the Chairmanship of Chief Engineer(EAP) at UPPWD Office to Review the Progress of preconstruction activities of Missing Link (Rath-Garautha), SH-42, Phase-II Roads & Stage-II Clearance of Phase-I Roads and the same was attended by the PWD Officials and Deputy Team Leader Mr. Sarwan Singh Saini. Minutes of Meeting (MoM) issued by the Authority vide letter No. 1878/Meeting/CEEAP/2022 Dated 30.08.2022.

**b. Site Visits Carried out during the Month**

**01.08.2022-** Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar and Sr. Bridge Engineer Mr. Rajiv Ranjan Verma on dated 01<sup>st</sup> August 2022 for Gola-Shahjahanpur project road and their observations notified to the Contractor (APCO) vide letter No. Egis India/LKO/UPCRNDP/2022/1891 Dated 04.08.2022.

**02.08.2022-** Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar and Sr. Bridge Engineer Mr. Rajiv Ranjan Verma along with Executive Engineer, P.W.D. Mr. Atul Kumar Sharma and Assistant Engineer, P.W.D. Mrs. Garima Srivastava on Dated 02<sup>nd</sup> August 2022 for Badaun-Bilsa-Bijnaour Road Project and their observations notified to the Contractor (GAWAR) vide letter No. Egis India/LKO/UPCRNDP/2022/1893 Dated 05.08.2022.

**08.08.2022-** Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar and Sr. Bridge Engineer Mr. Rajiv Ranjan Verma on dated 08<sup>th</sup> August 2022 for Hamirpur-Rath project road and their observations notified to the Contractor (APCO) vide letter No. Egis India/LKO/UPCRNDP/2022/1906 Dated 09.08.2022.

**10.08.2022** - Site visit carried out by the Deputy Team Leader Mr. Sarwan Singh Saini and Resident Engineer, Maintenance Team Mr. Anjani Kumar in order to accompany the Authority Representatives (Project Director and Superintending Engineer) during their site visit on 10.08.2022 for the Gola-Shahjahanpur project road.

**16.08.2022 and 17.08.2022** - Site Inspection of Maintenance Works by the Deputy Team Leader and Construction Safety Engineer on 16<sup>th</sup> and 17<sup>th</sup> August 2022 for Badaun-Bilsa-Bijnaour Road Project and their observations notified to the Contractor (GAWAR) vide letter No. Egis India/LKO/UPCRNDP/2022/1911 Dated 18.08.2022.

**30.08.2022-** Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar on dated 30<sup>th</sup> August 2022 for Hamirpur-Rath project road to analyze the severe damage of road due to Heavy Rain Hit by Flood and Backflow of Betwa River and reported to the Authority vide letter No. Egis India/LKO/UPCRNDP/2022/1933 Dated 31.08.2022. During the visit, Contractor (GHV) was also instructed to fill/rectify the paved shoulder and rain cuts immediately in order to avoid further damages to the paved shoulder.


**Site Inspection by the UPPWD Officials during the Month**

**10.08.2022-** Site visit carried out by the Authority Representatives (Project Director and Superintending Engineer) on 10.08.2022 for the Gola-Shahjahanpur project road accompanied by the Egis Representatives Deputy Team Leader Mr. Sarwan Singh Saini and Resident Engineer, Maintenance Team Mr. Anjani Kumar to inspect the site and tree plantation.

**15. Correspondence Management**

Important Correspondences and Minutes of the Meeting conducted are attached as Enclosure-1.

## 16. Construction Supervision Consultant's Mobilization

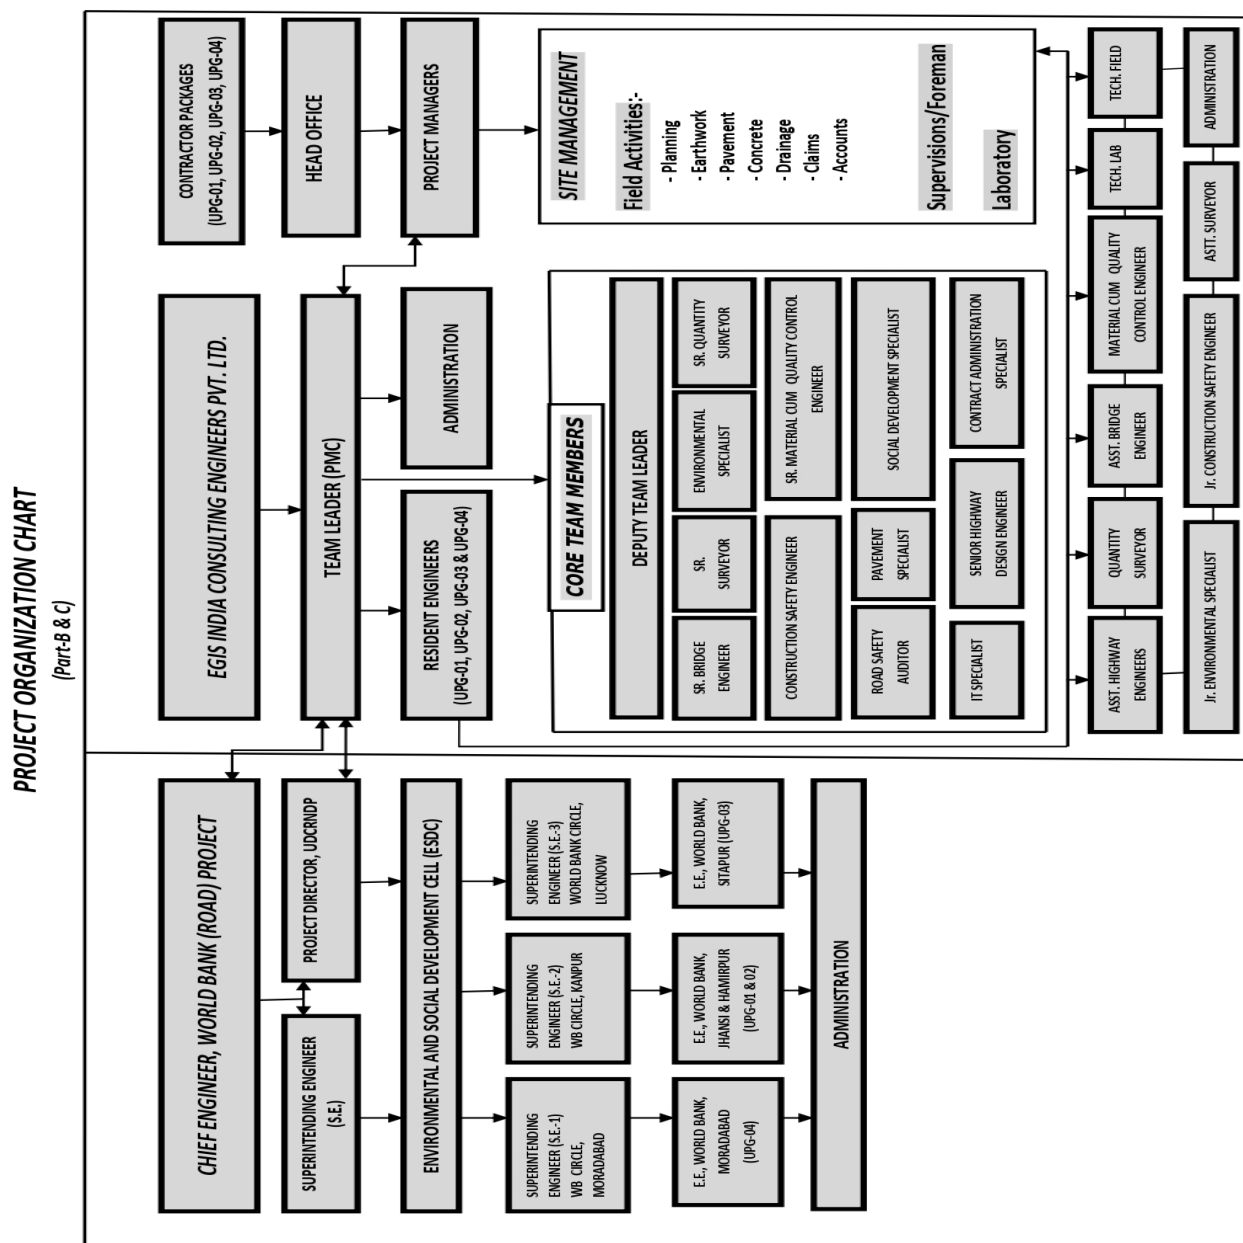

### a. Organization

The Construction Supervision Services for Phase-I Roads including EPC Contract Supervision is shown diagrammatically in the Construction Supervision Organization chart in Figure above:

**b. Consultant's Mobilization**
**i. Staff**

The table below shows Egis Staff mobilizations until the date of this report, together with the proposed durations of each staff member.

Position	Name	Duration (months)	Start Date	Remarks
<b>TEAM LEADER'S OFFICE</b>				
Team Leader	Mohd. Ayaz Beg	65.381	01.06.19	
Dy. Team Leader (Const. Mgmt. Specialist)	Mr. Sarwan Singh Saini	36	18.03.21	Part B & C services
Contract Administration Specialist	TBA	36	TBA	Part-C Services
Senior Highway Design Engineer	Mr. Sanjay Kumar	18		Part-C Services (Existing Staff of EGIS)
Senior Bridge Design Engineer (intermittent)	-	10		Part-C Services (Existing Staff of EGIS)
IT Specialist	Mr.Sanjay Ayyangar	36	10.09.19	Part B & C Services
Social Development Specialist	-	16.44	08.08.18	Part-C Services-
Road Safety Auditor	Mr. Bhushan Kumar Merigala	10		Part-C Services (Existing Staff of EGIS)
Pavement Specialist (Intermittent)	Mr. T. Someshwar Rao	11	03.09.19	Part-C Services
Senior Material cum Quality Control Specialist	-	45.5		
Construction Safety Engineer	Mr. Suraj Kumar Pathak	40	03.01.22	
Environment Specialist	Mr. Dev Brat Singh	45	15.03.18	Part-B & C Services
Senior Surveyor	-	16	05.03.18	Position not required.
Senior Bridge Engineer	Mr. Rajiv Ranjan Verma	39	01.05.20	Part-B Services
Senior Quantity Surveyor (Additional)	Mr. Anil Katiyar	42	19.02.20	Part-B Services
PMIS/Procurement Sub-professional	Mr. Deepak Pant	72	26.06.19	
Assistant Social Development Specialist (Additional)	Mr. Bikram Singh	10	11.09.19	
Office Manager cum Accountant	Mr. K.C.Joshi	72	14.05.18	
Computer Operator	Mr. Ashok Kumar Srivastava	72	15.04.15	
Office Assistant	Mr. Sunil Kumar	72	03.06.19	
Watchman	Mr. Rahul Kannojiya	72	01.07.22	

Notes: Project Works of all 4 Civil Contract packages are completed and O&M Phase started.

## ii. Vehicles

The Table below shows the Vehicles that have been deployed by the Egis for the use of Team Leader and Resident Engineers' Staffs in the project for the Supervision of Civil Work. The commercial registered Vehicles have been engaged with Drivers and fuel through vendors. Statutory Permit, Routine Service and Repairs for the Vehicles will be carried out by the Vendors.

S. No.	Vehicle Type	Vehicle No.	Start Date	Remarks
<b>TEAM LEADER'S OFFICE (LUCKNOW)</b>				
1	MARAZZO	UP-32 LN 6457	13.08.2019	
2	TATA AMAZE	UP-32 LN 2888/UP-32 RN 6588	23.07.2018	Vehicle UP-32 LN 2888 replaced with from UP-32 RN 6588 on 08.08.2022
<b>CONTRACT PACKAGE- UPG/01 HAMIRPUR – RATH</b>				
1	Dzire	UP-93 AR 8893	01.05.2020	
<b>CONTRACT PACKAGE – UPG/03 GOLA - SHAHJAHANPUR</b>				
1	BOLERO	UP-27 AT 8925	01.05.2022	
<b>CONTRACT PACKAGE –UPG/04 BADAUN – BILSI - BIJNAOUR</b>				
Nil				

## iii. Offices

Team Leader Office has been set up in Lucknow near to Client's Office.  
 Address is: Office of the Team Leader/Authority Engineer,  
 Egis India Consulting Engineers Pvt. Ltd.  
 House No.3/138, Vishal Khand-3, GomtiNagar,  
 Lucknow, UP-226010, Phone: 0522 - 4952905,  
 Email: egis\_upcrndp@egis-india.com; ayaz.b@egis-india.com

### Site Office Addresses:

The supervision of Maintenance works for all four completed Phase-I roads is now being monitored with limited Field staffs by the single Resident Engineer from Team Leader Office, Lucknow from 01.05.2022 with assistance of TL and staffs.

<b><u>Contract Package – UPG/01</u></b>  <b>Hamirpur – Rath Section of SH-42</b> Project Site office and Staffs (Except AHE) are demobilized from 1 <sup>st</sup> May 2022.	<b><u>Contract Package- UPG/02</u></b>  <b>Garautha–Chirgaon Section of SH-42</b> Project Site office and Staffs (Except AHE) are demobilized from 31 <sup>st</sup> December-2020.
<b><u>Contract Package – UPG/03</u></b>  <b>Gola – Shahjahanpur Section of SH-93</b> Project Site office and Staffs (Except AHE) are demobilized from 1 <sup>st</sup> May-2022.	<b><u>Contract Package – UPG/04</u></b>  <b>Badaun–Bilsi–Bijnaour Section of SH-51</b> Project Site office and Staffs (Except AHE) are demobilized from 1 <sup>st</sup> February-2022.

## **CONTRACT PROJECT ACTIVITIES**

### **17. CONSTRUCTION PACKAGE –UPG-02**

#### **a. Introduction**

Contract Package UPG-02, Up-gradation (Widening/Strengthening) of Garautha-Chirgaon Section of SH-42 from Km. 118+600 to Km. 167+745, has been awarded to M/s NKC Projects Pvt. Ltd., Gurgaon, for a Contract Amount of INRs 189,99,99,491.00. The Contract Agreement No.100/UPCRNDP /CEEAP/2016-17 was signed on 4<sup>th</sup> January 2017.

The project works are divided into two parts,

PART-1 Completed on 31<sup>st</sup> October 2020 and completion certificate issued by the Engineer and the site was handed over to the Client, however as the contract includes Part-2 DLP/Maintenance works for 5 Years, the site was handed over back to the same contractor NKC Projects Pvt. Ltd.

PART-2 Includes maintenance for 5 Years after taking over Part-1 works, which started on 1<sup>st</sup> November 2020

Contractor has been reminded to prepare and submit Addendum/Supplementary Agreement for the Extension of Contract Period vide our letter no. Egis India/LKO/UPCRNDP/2022/1929 Dated 30.08.2022, however submission is awaited till date.

This Monthly Operation and Maintenance Report cover the Month of August 2022 and summarize the activities up to end of this month.

Contract Package	UPCRNDP/UPG/02/2014 Garautha-Chirgaon Road (SH-42)		
	PART-1	PART-2	Remarks
<b>Project Length (In Km)</b>	49.145	49.145	
<b>Project Cost (In Cr.) (As per CA)</b>	185.77	4.22	
<b>Project Cost (In Cr.) (Actual)</b>	183.92	4.22	
<b>Scheduled Start Date (As per CA)</b>	15-01-2018	15-10-2020	24 months for Part-1 works and 5 Years for Part-2 works including 1 yrs. of DLP
<b>Scheduled Completion Date (As per CA)</b>	14-01-2020	14-01-2025	
<b>Actual Start Date</b>	15-01-2018	01-11-2020	Part-1 works delayed by 9.5 months for completing additional works at Vill-Gursarai and Sultanpura;
<b>Actual Completion Date</b>	31-10-2020	31-10-2025	

- Part-1 works are completed on 31<sup>st</sup>October 2020 and Part-2 O&M works commenced on 01<sup>st</sup>November 2020.
- Contractor's DLP responsibility was up to 31<sup>st</sup> October 2021(from the completion date of part-I works) however extended DLP was completed on 31<sup>st</sup> December 2021 and the Defect Liability Certificate (DLC) issued to the Contractor vide Engineer's letter No. Egis India/HO/UPCRNDP/78573/2022 Dated 17.01.2022.
- The responsibility of routine maintenance will be continued till 31<sup>st</sup>October 2025.

**b. Salient Features of Contract**
**Salient Features of the Contract are enclosed as Annexure-A- Contract Data**

The works were executed under FIDIC (5<sup>th</sup> Edition) Conditions of Contract. The work involves improvement of State Highways including geometric improvements and realignments to standard 2-lane carriageway with Paved Shoulders and verges.

**Consultant Mobilization:**

The supervision of Maintenance works is being monitored by the Resident Engineer from Team Leader Office, Lucknow from 01.05.2022 with assistance of TL and staffs.

**Staff Mobilization**

Asst. Highway Engineer : Mr. Sanjeev Sharma (at Project Site)

**Operation and Maintenance Centre Establishment**

Contractor for O&M activities has relocated his office in village-Gursrai in rented house in May-21. The O&M activities are being operating from new office.

Base Camp Office Address:

M/S NKC Projects Pvt. Ltd.

Plot No. 218, Village- Nehar Kothi Gursarai, Moth Road

Tehsil- Tehrauli, Dist.- Jhansi (UP)- 284202

Mob no- 9696991471 ( Mr. Sameer Ranjan Moharana)

**List of Contractor Staff Mobilized for Maintenance Period**

Sl.	Name	Designation	Remarks
1	Mr. Sachinder Singh	Project-Head	Available at HO
2	Mr. Sachin Gautam	Project- Incharge	Available at Project Site
3	Mr. Kuldeep Singh	Highway Supervisor	Available at Project Site
4	Mr. Samir Mohana	Highway Foreman	Available at Project Site

**List of Equipment Mobilized for Maintenance Period**

List of Machinery and Equipment which to be available for O&M period is enclosed Refer **Annexure-B**

**Correspondence during O&M Period**

**Resident Engineer for Maintenance Team is monitoring the scheduled Maintenance activities of the package from 1<sup>st</sup> May'22 with the help of AHE based at UPG-02 project site.** Consultants visit the project site of Garautha-Chirgaon Road on regular intervals and notify the observations (along with photographs) for immediate rectifications in writing with evidence/photos. The Contractor is responsible for the DLP/maintenance period for 5 years

**Materials**

Procurement of materials for Maintenance Activities is being carried as per necessity at site.

**18. Work Progress****i. Design and Drawings**

As Built Drawings Approved and required copies have been issued to the Client and Engineer.

**ii. Maintenance Work Programme**

The Contractor's Maintenance program as per Clause A-1.4 for the month of September 2022 will be submitted for AE's review.

**iii. Monthly Maintenance Payment Certificate**

The Contractor has submitted Maintenance Payment Certificate No. 07 to 08 vide his letter Nos. NKC/HO/GC/2022-23/192 & 193 Dated 08.08.2022 and recommended by TL office on Dated 22.08.2022 vide letter No. Egis India/LKO/UPCRNDP/2022/1913 & 1914 of IPC-07 to IPC-08 respectively up to the July 2022.

PMC instructed Contractor to submit the Maintenance Payment Certificate as per Special Conditions of Contract (SCC) Clause 42.7 of Contract Agreement.

**iv. Physical Progress**

The physical progress of Maintenance Activities is being monitored, Refer **Annexure-C**. Further Progress details may be found in **Annexure-D**, Logistic Plan

**v. Quality Control/Quality Assurance**

Field Laboratory Demobilized in June 2020. However all materials used for permanent maintenance works are checked by AE for source approvals.

**vi. Meetings & Site Inspections**

- Regular Site Visits are being conducted by AE and Inspection reports were sent with observations to the Contractor in order to conform the safety of road users.
- Site visits carried out by the Assistant Highway Engineer Mr. Sanjeev Sharma on dated 03.08.2022, 12.08.2022 & 15.08.2022 and Inspection and Observations Report issued to the Contractor for compliance vide Egis Letter No. Egis India/RE UPG-02/UPCRNDP/014/2022 Dated 16.08.2022.

**vii. Key Issues**

- Contractor strictly instructed to ensure that the 2 Nos. Toilet Blocks at Truck Lay Bys must be functional 24X7 with running water and Power.
- At Ch. 139+600, the Jal Nigam Department is constructing a box culvert for irrigation canal crossing by demolishing the newly constructed road. This has been intimated to the Authority and to the Concerned Department of UP Govt. for further necessary action. The

Excavation by External Agency is up to 15m in depth, which causes disturbance to the adjacent part of the Project Road. The Road Project Contractor of UPPWD will NOT be responsible for maintenance of this section of road, which has to be maintained by the Irrigation Dept. and a MOU has been agreed by all parties. The AE has written to the Client expressing the safety concerns due to embankment height increased to almost 15 mtrs and therefore, the Irrigation Department Contractor must provide all safety measures for this section of road to prevent fatal accidents. The above stretch opened for the traffic on Grannular without Paving of Bitumineous Layer and Safety Measures.

- The Contractor has taken temporary measures to seal the Longitudinal minor Cracks developed in the paved shoulder from ch.120+800 to ch.124+650 for which the Contractor to submit methodology and sealant material for permanent repair immediately after rainy season.
- Metal Beam Crash Barriers have not been connected with RCC Crash Barriers at Bridge locations. Contractor has to connect the MBCB to RCC Crash Barriers as soon as the connectors are delivered to prevent any accidents. In the meantime the Contractor instructed to immediately place sand bags with reflective tape at these locations.
- Concrete Crash Barrier painted over by Local Residents at many locations to be repainted black and white as per Contract requirement for structure visibility for safety of road users.
- Local residents dumped building material on road side and footpath, instructed Contractor to inform Police/Client/PMC immediately to prevent serious accidents.

viii. **Weather**

Weather report for the reported period is shown in **Annexure-E**.

## 19. CONTRACT PACKAGE UPG-01

### a. Introduction

Contract Package **UPG-01**, Engineering, Procurement and Construction Contract for Up-gradation and Maintenance of Hamirpur to Rath Section of SH-42 from design Ch.2.065 (PWD Km 2.065) to Ch.74.850 (PWD Km 74.255) for total length 72.785 Km in the State of Uttar Pradesh, has been awarded to **M/s GHV (India) Pvt. Ltd.**, through International Competitive Bidding (ICB) norms for the Up-gradation and development. The Contract Agreement No.115/UPCRNDP/UPG/01/2019-20 was signed on 19<sup>th</sup> June 2019 and the EPC Contract Amount is of **INRs 262,39,50,000/-** (Rupees Two Hundred Sixty-Two Crore Thirty-Nine Lac Fifty Thousand Only). The Revised Completion cost of Project of Civil Works is of **INRs. 275,65,00,741/-** (Rupees Two Hundred and Seventy-Five Crore Sixty-Five Lakhs Seven Hundred Forty-One Only). The Total Maintenance Cost for 5 years is **Rs.10,33,68,778/-** (Rupees Ten Crore Thirty-Three Lakh Sixty-Eight Thousand Seven Hundred and Seventy-Eight Only).

This **Monthly Inspection Report** covers the Month of August 2022 and summarizes the activities up to end of this month.

Contract Package	Length (Km)	Completion Period (as per Contract)	Contract Agreement Date	Appointed Date (as per Contract)	Actual Completion Date	O&M Period/ DLP Period/ Commencement Date
UPCRNDP/UPG/01/2018 Hamirpur - Rath Road (SH-42)	72.785*	24 Months	19 <sup>th</sup> June 2019	25 <sup>th</sup> June 2019	12 <sup>th</sup> August 2021	5 Years/12 <sup>th</sup> July 2021

\*Revised Length for Maintenance is 72.071 Km as 714 m length (KM 63+026 to KM 63+740) de-scoped by UPPWD at interchange of Bundelkhand Expressway.

Sl. No.	Affected Chainage		Affected Length (Mtr.)	Govt. Agency
	From	To		
1	63.026	63.740	714	UPEIDA
<b>Total Length in Mtr.</b>			<b>714</b>	

The commencement of Maintenance has been started on 12<sup>th</sup> July 2021 and this report covers all the Maintenance activities of the Project Site.

The project work includes the Up-gradation (Widening/Strengthening) of existing carriageway as per contract specifications under EPC contract and the completed road works required. The maintenance period of 5 years including Defect Liability Period after issuance of projects' Provisional Completion Certificate (PCC).

Contractor has been reminded to prepare and submit Addendum/Supplementary Agreement for the Extension of Contract Period vide our letter No. Egis India/LKO/UPCRNDP/2022/1928 Dated 30.08.2022, however submission is awaited till date.

Authority Engineer has issued to the Contractor:

**Provisional Completion Certificate:** Authority Engineer issued Provisional Completion Certificate to Contractor vide letter Ref. No. Egis India/HO/UPCRNDP/71132/2021 Dated 13/07/2021 with effect from 12/07/2021.

**Project Completion Certificate:** Authority Engineer issued Completion Certificate to Contractor on vide letter Ref. no Egis India/HO/UPCRNDP/UPG-01/72578/2021 dated 16/08/2021 with effect from 12/08/2021.

Maintenance & DLP	Routine maintenance of the Project road for a period of 5 years commencing from the date of Provisional Completion Certificate (PCC) as per Contract agreement (Sub-clause 14.1.1) of Article 14 and (Sub-clause 17.1.1) of Article 17 respectively.	O&M Phase started from 12 <sup>th</sup> July 2021
-------------------	--	---

Salient Features of the Contract is Enclosed, **Refer Annexure-A- Contract Data.**

**b. Description of Works**

The Project works under EPC agreement involves two phases to execute the assigned activities.

**Maintenance & DLP** involves protection, repair and maintenance of constructed road for 60 months (1826 days) from the date of Provisional Completion Certificate.

**c. Consultant Mobilization**

The supervision of Maintenance works for all four completed Phase-I roads is now being monitored with limited Field staffs by the single Resident Engineer from Team Leader Office, Lucknow from 01.05.2022 with assistance of TL and staffs.

**Staff Mobilization**

Asst. Highway Engineer : Mr. Ravish Kumar (at Project Site)

**d. Construction Activities: Focuses on O&M Works**

**i. Mobilization of Contractor**

**1. Base Camp Establishment**

Contractor has shifted his Base Camp establishment for the O&M Phase of activities from Ch.57+000 LHS, Village-Bihuni to Ch. 52+800 LHS, Village-Muskara.

Base Camp Office Address:

GHV (INDIA) PVT.LTD,  
KissanBandhu Campus,  
Ch. 52+800 LHS Muskara,  
Hamirpur – 210506  
PH No. 7060099481

**2. Human Resources**

Contractor has mobilized Key Staff as given below;

Sl.No.	Designation	Name	Status
1	Project head from HO	Mr. Imran Siddhiqui	Available
2	Project Incharge	Mr. Anurag	Available
3	Highway Supervisor	Mr. Pankaj	Available

**3. Equipment and Machinery**

List of Key Plant and Equipment which are available for O&M period is enclosed Refer **Annexure-B**

**4. Material**

Procurement of material from approved sources for Maintenance Activities is in progress as per necessity at site.

**e. Work Progress****i. Design and Drawings**

Contractor has submitted “As Built Drawings” vide letter No.GHV/Site/SH-42/Rath/922 Dated 12.02.2022 which have been approved by the AE as all corrections and comments incorporated and submitted 1 copy of A2 size on Polyester paper to the Authority vide letter No. Egis India/LKO/UPCRNDP/2022/1772 Dated 17.05.2022.

**ii. Project Completion /Operation and Maintenance**

Rev.01 O&M Manual received vide letter ref. GHV/Site/SH-42/Rath/829 dated 03<sup>rd</sup> June 2021 has been reviewed and approved by the PMC/AE vide letter ref. Egis India/LKO/UPCRNDP/2021/1324 Dated 15<sup>th</sup> June 2021. Final O&M Manual received from the Contractor (GHV) vide letter No. GHV/Site/SH-42/ Rath/829 Dated 09.07.2021 and submitted to the Authority vide letter No. Egis India/LKO/UPCRNDP/ 2021/1361 Dated 13.07.2021.

**iii. Maintenance Work Programme**

Contractor has submitted the Maintenance Program as per Clause 14.3 of Article 14 of Contract Agreement for the month of September 2022.

**iv. Monthly Maintenance Statement (MMS)**

The Contractor has submitted the Monthly Maintenance Statement MMS 10 to MMS 12 (IPC 04) for the period from 1<sup>st</sup> April 2022 to 30<sup>th</sup> June 2022 vide letter No. GHV/site/SH-42/RATH/966 Dated 18.07.2022 and the same was certified and recommended to the Authority vide letter No. Egis India/LKO/UPCRNDP/2022/1874 Dated 21.07.2022.

Authority Engineer instructed Contractor to submit the Monthly Maintenance Statement as per Clause 19.6 of Contract Agreement.

**v. Physical Progress**

Physical Progress of Maintenance Activities is being monitored Refer **Annexure-C**, further progress details found in **Annexure –D**, Logistic Plan for O&M Phase.

**f. Quality Control / Quality Assurance**

Field laboratory demobilized in June-2021 any testing during the DLP to be carried out by Approved Independent Labs.

**g. Meetings & Site Inspections**

- Regular Site Visits are being conducted by the AHE and Inspection reports with observations were issued to the Contractor in accordance to the conformity of Safe use of Project Highway.
- Site visit carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar & Sr. Bridge Engineer Mr. Rajiv Ranjan Verma on dated 08.08.2022 and Inspection and Observations Report issued to the Contractor for compliance vide Egis Letter No. Egis India/LKO/UPCRNDP/2022/1906 Dated 09.08.2022.

- Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar on dated 30<sup>th</sup> August 2022 for Hamirpur-Rath project road to analyze the severe damage of road due to Heavy Rain Hit by Flood and Backflow of Betwa River and reported to the Authority vide letter No. Egis India/LKO/UPCRNDP/2022/1933 Dated 31.08.2022. During the visit, Contractor (GHV) was also instructed to fill/rectify the paved shoulder and rain cuts immediately in order to avoid further damages to the paved shoulder.

#### **h. Key Issues**

##### **General Site Related Issues:**

- Local residents dumped building material on road side and footpath, instructed Contractor to inform Police/Client/PMC immediately to prevent serious accidents.
- Contractor replanting of dead tree saplings work in progress.
- Contractor to employ women for general maintenance works.
- Contractor reminded that all Maintenance Works on the Live Carriageway MUST be barricaded with plastic water filled barriers with all advance warning signs and a minimum of 2 flagmen to prevent fatal accidents and workers in the work zone MUST wear full PPE.
- Contractor is progressing with the cleaning of all inlets and outlets of the culverts and bridges for free flow of water and prevent flooding. Also is cleaning inside of RCC Drains and the weep holes to prevent flooding of the carriageway and the adjacent properties.
- The Contractor has been instructed to investigate further the Cracks developing in the Pavement Quality Concrete (PQC) and should submit a revised detailed Method Statement for repairing the cracks with alternative materials for durability.
- Reinstate the aprons of culverts with boulders at the inlets and outlets.
- Faded Road Marking at various locations of highway to be carried out in order to guide the traffic and safety of road user to prevent accident which is in progress but due to rainy season Contractor unable to expedite the road marking.
- The Contractor instructed to make all 4 No: Toilet Blocks functional 24X7 with running water and power and clean them regularly. However, the Contractor is to handover to the local municipality for keeping them open 24X7.

#### **i. Weather**

Weather Report for the reported period is shown in **Annexure-E**.

## 20. **CONTRACT PACKAGE UPG-03**

### a. **Introduction**

Contract Package **UPG-03**, Engineering, Procurement and Construction Contract for Up-gradation (Widening/Strengthening) of Gola -Shahjahanpur Section of SH-93 from design Ch. 1+280 to Ch. 58+580, has been awarded to **M/s APCO Infratech Pvt. Ltd.**, Gurgaon, for a Contract Amount of **INRs 356,90,00,000.00**.

The Contract Agreement No.116/UPCRNDP/CEEAP/2019-20 were signed on 26.06.2019 and appointed date is 11.11.2019.

Sl. No.	Contract Package	Length (Km)	Completion Period (as per Contract)	Contract Agreement Date	Commencement Date (as per Contract)	Actual Completion Date	O&M Period/ DLP Period/ Commencement Date
1	UPCRNDP/UPG/ 03/2014 Gola-Shahjahanpur Road (SH-93)	57.535*	24 Months	26 <sup>th</sup> June 2019	11 <sup>th</sup> November 2019	15 <sup>th</sup> March 2022	15 <sup>th</sup> March 2022

\* Revised length for Maintenance is 56.388 Km as 1147m length has been de-scoped by UPPWD due to overlapping of some sections of Proposed Road was completed by other Government Agency.

Sl. No.	Affected Chainage		Affected Length (Mtr.)	Govt. Agency
	From	To		
1	29.515	30.317	802	NH Division
2	59.035	59.380	345	NH Division
<b>Total Length in Mtr.</b>			<b>1147</b>	

The Cumulative Physical Progress achieved 100% on 15<sup>th</sup> March, 2022 and Financial Progress is 96.66% up to 12<sup>th</sup> March, 2022. The Authority Engineer issued to the Contractor the Completion Certificate on dated 15<sup>th</sup> March 2022 as all the works were completed within the Extension of Time granted to the Contractor (Via CE, PWD Email dated 20.06.2022) due to the Force Majeure Event caused by the Pandemic COVID-19.

Contractor submitted Addendum/Supplementary Agreement for the Extension of Contract Period forwarded to the Authority vide our letter No. Egis India/LKO/UPCRNDP/2022/1854 Dated 06.07.2022. Supplementary Agreement signed by both the parties UPPWD and Contractor.

The Project work includes the Up-gradation (Widening/Strengthening) of existing Carriageway, that is 2 lanes with paved shoulder in the stretch from Design Chainage (1+280) to (59+380), and maintenance and Defect Liability Period (DLP) for 5 years. Also a major bridge with six spans total span width 116 m and 4 No: minor bridges with spans over 40 m to be reconstructed.

### b. **Salient Features**

**Project Completion Certificate:** Authority Engineer issued Completion Certificate to Contractor on vide letter Ref. no Egis India/HO/UPCRNDP/UPG-03/81183/2022 Dated 29/03/2022 with effect from 15/03/2022.

Maintenance & DLP	Routine maintenance of the Project road for a period of 5 years commencing from the date of Completion Certificate (CC) as per Sub-clause 17.1.1 of Article 17 of Contract Agreement (CA).	O&M Phase started from 15 <sup>th</sup> March 2022
-------------------	--	--

Salient Features of the Contract are enclosed as **Annexure-A-** Contract Data.

**c. Description of Works**

The works are being executed under EPC agreement. The work involves improvement of SH-93 including geometric improvements and realignments to standard 2-lane carriageway with Paved Shoulders, as Typical Cross Section (TCS) of Contract.

**Maintenance & DLP** involves protection, repair and maintenance of constructed road for 60 months which commenced from the date of issue of provisional Completion Certificate or from the date of Completion Certificate in case no Provisional Completion Certificate issued to Contractor as per Clause 17.1.1 of Article 17 of Contract Agreement.

For this package UPG-03, NO Provisional Completion Certificate was issued to the Contractor and Completion Certificate issued directly on 15.03.2022 after completion of Project in all respect therefore, 5 years maintenance period started from 15.03.2022

**d. Consultant Mobilization**

The Supervision of Maintenance Works for all four completed Phase-I roads is now being monitored with limited Field staffs by the single Resident Engineer from Team Leader Office, Lucknow from 01.05.2022 with assistance of TL and staffs.

**e. Staff Mobilization**

Asst. Highway Engineer : Mr. Ram Pratap Singh (at Project Site)

**f. Construction Activities: Focuses on O&M Works**

**i. Mobilization of Contractor**

**1. Operation and Maintenance Centre Establishment**

Contractor has continued implementation of O&M Activities from his established Base Camp Office at Ch.39+600 LHS, Village-Kheriyaj at Lakhanpur.

Base Camp Office Address:  
M/S APCO Infratech Pvt. Ltd.  
KM Stone -39, Sh-93, Village Kheriyajat Lakhanpur,  
Post-Gorkan, Tehsil-Mohammadi,  
Dist.-Lakhimpur Kheri

**2. Human Resources**

Contractor has mobilized Key Staff listed in table below;

Sl. No.	Designation	Name	Status
1	O&M In-charge	Mr. Sunil Rathor	Based at HO-Lucknow
2	O&M Engineer	Mr. Kuldeep Mohanto	Available at Project site
3	Admin Manager	Mr. Rakesh	Available at Project site
4	Highway Supervisor	Mr. Sandeep Yadav	Available at Project site
5	Highway Supervisor	Mr. Gaurav Shukla	Available at Project site

### 3. **Plant and Machinery**

Contractor has started demobilization of following Construction Plants from Base Camp location Ch. 39+600 (LHS).

Sl. No.	Plant Mobilized	No.	Location	Make & Capacity	Status
1	Concrete Mix Batching Plants	01	Ch.39+600LHS	30Cum/Hr.	Idle/ dismantling
2	Wet Mix Plant	01	Ch.39+600 LHS	160 TPH	Idle/ dismantling
3	Hot Mix Plant	01	Ch.39+600 LHS	200 TPH	Idle/ dismantling
4	Crushers	-	Not Established		NA

List of equipment which is available for O&M Period -**Refer Annexure-B-Equipment & Machinery Details.**

### 4. **Material**

No Material Procurement needed at this stage. Sufficient materials stored at base camp center for maintenance activities.

### g. **Work Progress**

#### i. **Design and Drawing**

Contractor has been reminded to re-submit the “As Built Drawing of Structures and Highway” vide letter No. Egis India/LKO/UPCRNDP/2022/1926 Dated 29.08.2022 after reviewing by the Design Consultant however re-submission is awaited till date.

#### ii. **Maintenance Work Programme**

Maintenance Program for the current month was received by AE as per Article 14.3 of Contract Agreement. AE has monitored the O&M activities as per Program.

#### iii. **Financial Progress**

Contractor has submitted revised Final Payment Statement (IPC-17) vide letter No. APCO/WB-UPCRNDP/EGIS/ST/767 Dated 15.07.2022 without submitting rate analysis of Reclaimed Asphalt Pavement (RAP) material used in the project work. Contractor had been instructed to submit the rate analysis vide letter No. Egis India/LKO/UPCRNDP/2022/1879 Dated 27.07.2022 and Egis India/LKO/UPCRNDP/2022/1902 Dated 09.08.2022 which is awaited till date. Once the Final Bill submitted with rate analysis then the same shall be processed and recommended to the Authority by the AE.

#### iv. **Monthly Maintenance Statement (MMS)**

The Monthly Maintenance Statement MMS 05 for the period from 01<sup>st</sup> July'2022 to 31<sup>st</sup> July'2022 submitted by the Contractor vide letter No. APCO/WB-UPPWD/EGIS/ST/772 Dated 16.08.2022 has been under review of the Authority Engineer.

#### v. **Physical Progress**

The physical Progress of Maintenance Activities is being monitored as per listed works Monthly Inspection and Maintenance Program. **Refer Annexure-C.**

**Further Progress details presented in:**

**Annexure-D, Logistic Plan for O&M Phase**

**h. Meetings & Site Inspections**

- Daily Routine Site Inspection for monitoring maintenance works carried out by AHE with Contractor's Field Staff.
- Site visit carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar & Sr. Bridge Engineer Mr. Rajiv Ranjan Verma on dated 01.08.2022 and Inspection and Observations Report issued to the Contractor for compliance vide Egis Letter No. Egis India/LKO/UPCRNDP/2022/1891 Dated 04.08.2022.
- Site visit carried out by the Deputy Team Leader Mr. Sarwan Singh Saini and Resident Engineer, Maintenance Team Mr. Anjani Kumar in order to accompany the Authority Representatives (Project Director and Superintending Engineer) during their site visit on 10.08.2022 for the Gola-Shahjahanpur project road.

**i. Key and Potential Issues**

- The Contractor to carry out regular inspection jointly with AE and take action for clearing any debris and report any unusual occurrence on daily basis.
- The Contractor instructed to submit the AS BUILT DRAWINGS (ABD) in accordance with Contract Agreement (2 copies of A2 Size on Polyester paper). Earlier Contractor has submitted ABD in A3 size on normal paper for AE's review, the same were reviewed and returned with comments. Contractor to incorporate the comments in the final ABD.
- The Contractor has started to replace all dead tree saplings with tree guards in order to take advantage of monsoon rain season.
- Contractor instructed to submit the Consolidated Waste Management Plan before final closure/expiry of land owner's agreement for both Camps.
- Any Chain-link fence damaged in the Reserve Forest to be repaired immediately by the Contractor to prevent the Wild Animals crossing the live carriageway.

**j. Weather Report**

Weather report for the reported period is shown in **Annexure-E**

## 21. CONTRACT PACKAGE UPG-04

### a. Introduction

Contract Package **UPG-04**, Engineering, Procurement and Construction Contract for Up-gradation (Widening/Strengthening) of Badaun-Bilsi-Bijnaour Section of SH-51 from Km.58+400 to Km.137+820, has been awarded to **M/s GAWAR Construction Ltd., Gurugram** through ICB Bidding norms for up-gradation and development. The Contract Agreement No.117/UPCRNDP/CEEAP/2019-20 was signed on 5<sup>th</sup> July 2019 and the EPC Contract Price is **INRs 334,00,00,080.00**.

**Note:** Revised length for Maintenance is 78.309 Km as 816 m length has been de-scoped from the Contractor's O&M Responsibility as the State Irrigation Department took permission from UPPWD for Construction and crossing the irrigation canals at 4 locations across the completed Project highway.

Sl. No.	Affected Chainage		Affected Length (Mtr.)
	From	To	
1	93.709	93.865	156
2	105.150	105.362	212
3	107.729	108.053	324
4	108.363	108.487	124
<b>Total Length in Mtr.</b>			<b>816</b>

This **Monthly Inspection Report** covers the activities up-to the current month.

Sl. No	Contract Package	Length (Km)	Completion Period (As per Contract)	Contract Agreement Date	Commencement Date (As per Contract)	Actual Completion Date	O&M Period/DLP Period/ Commencement Date
1.	ICB No. UPCRNDP/UPG/04/2018 Badaun-Bilsi-Bijnaour Road (SH-51)	79.125	730 days	5 <sup>th</sup> July 2019	4 <sup>th</sup> November 2019	10 <sup>th</sup> January 2022	5 Years / 10 <sup>th</sup> January 2022 to 9 <sup>th</sup> January 2027

The Cumulative Physical Progress achieved 100% as on 31<sup>st</sup> January 2022 and Financial Progress is 99.60% up to January 2022.

**The Completion Certificate was issued by the Authority Engineer Dated 10<sup>th</sup> January 2022 vide letter No. Egis India/HO/UPCRNDP/UPG-04/78908/2022 Dated 28.01.2022.**

Maintenance & DLP	Routine maintenance of the Project road for a period of 5 years commencing from the date of Completion Certificate (CC) as per Sub-clause 17.1.1 of Article 17 of Contract Agreement (CA).	O&M Phase started from 10 <sup>th</sup> January 2022.
-------------------	--	---

The Project work includes the Up-gradation (Widening/Strengthening) of existing carriageway maintenance and Defect Liability Period (DLP) for 5 years.

Contractor submitted Addendum/Supplementary Agreement for the Extension of Contract Period forwarded to the Authority vide our letter No. Egis India/LKO/UPCRNDP/2022/1884 Dated 30.07.2022. Supplementary Agreement signed by both the parties UPPWD and Contractor.

**b. Salient Features**

Salient Features of the Contract are enclosed as **Annexure-A- Contract Data**.

**c. Description of Works**

The Project works under EPC agreement which involves two phase to execute the assigned activities. Civil Work was assigned for Up-gradation and Strengthening the project road length of SH-51 in 24 months of period from the date of appointment. Contractor has achieved and completed the entire project works in designated four Milestones.

**Maintenance & DLP** involves protection, repair and maintenance of constructed road for 60 months which commenced from the date of issue of Completion Certificate.

**d. Mobilization of Consultant**

The supervision of Maintenance works for all four completed Phase-I roads is now being monitored with limited Field staffs by the single Resident Engineer from Team Leader Office, Lucknow from 01.05.2022 with assistance of TL and staffs.

**e. Staff Mobilisation**

Asst. Highway Engineer : Mr. Pramod Kumar Singh (at Project Site)

**f. Construction Activities: Focuses on O&M Works**
**Mobilization of Contractor**
**1. Base Camp Establishment**

Contractor has continued O&M activities from the existing Base Camp Office which was established for Construction Phase at Ch.102+200LHS, Village-Dehpa.

<b>Base Camp office Address for Civil works: Demobilized and Closed in February-2022</b>	<b>New Base Camp Office Address for Monitoring O&amp;M Works:</b>
GAWAR Construction Ltd. Village-Dehpa, P.O – Dehpa, Teh&Dist-Sambhal (U.P)-244302	GAWAR Construction Ltd C/o Md Navi, Village- Fatehpurdev, P.O-Dehpa, The & Dist-Sambhal (U.P)-244302 Ph. No. 63961-77256

**2. Human Resources**

The Contractor mobilised key staff is listed in table below;

<b>Sl.</b>	<b>Designation</b>	<b>Name</b>	<b>Status</b>
1	Sr. Project Manager	Mr. Vivek Sharma	Available at Project Site
2	Admin Manager	Mr. Naresh kumar	Available at Project Site
3	Highway Supervisor	Mr. Raghvendra Sharma	Available at Project Site
4	Highway Supervisor	Mr. Shashikant Sharma	Available at Project Site

**3. Equipment and Machinery during Maintenance**

List of Key Plant and equipment's which are available for O&M Period is enclosed, **Refer Annexure-B-Equipment & Machinery** Details.

**4. Material**

Sufficient materials are stored at O&M Center for Maintenance Activities.

**g. Work Progress****i. Design and Drawings**

Contractor has been reminded to re-submit the “As Built Drawing of Structures and Highway” vide letter No. Egis India/LKO/UPCRNDP/2022/1927 Dated 29.08.2022 after reviewing by the Design Consultant however re-submission is awaited till date.

**ii. Maintenance Work Programme**

Maintenance Program for the current month was received by AE as per Article 14.3 of Contract Agreement. AE has monitored the O&M activities as per Program.

**iii. Financial Progress**

Instructed Contractor to submit the Final Payment Statement for completed Civil Works as per the Contract Agreement vide our letter no. Egis India/LKO/UPCRNDP/2022/1822 Dated 11.06.2022 and Rate analysis of Reclaimed Asphalt Pavement (RAP) material used in the project work. Contractor had been instructed to submit the rate analysis, however submission is awaited till date.

**iv. Monthly Maintenance Statement (MMS)**

The Contractor has been instructed to submit the initial Monthly Maintenance Statement along with the Monthly Maintenance Program & requisite documents for the activities carried out during O&M phase in order to certify the Maintenance Payment Certificate however no submission by the Contractor till date.

**v. Physical Progress**

Physical Progress of Maintenance Activities is being monitored Refer **Annexure-C**, further progress details found in **Annexure-D**, Logistic Plan for O&M Phase.

**vi. Quality Control / Quality Assurance**

Contractor instructed to submit the Consolidated Waste Management Plan before final closure/expiry of land owner's agreement for both Camps.

**vii. Common Property Resources (CPRs)**

Cost Estimate of 11 Nos. Common Property Resources (CPRs) Structures Amounting INR 37,25,115.00 (Thirty Seven Lacs Twenty Five Thousand One Hundred Fifteen Only) were reviewed and recommended to the Authority for approval as per the Annex-1(Schedule-B) Sub-Clause 17.1 & Article 9.2(a) of the Contract Agreement vide Egis Letter No. Egis India/LKO/UPCRNDP/2022/1612 Dated 02.02.2022 and the same again requested to the Authority vide letter No. Egis India/LKO/UPCRNDP/2022/1866 Dated 15.07.2022 however approval from the Authority is awaited till date.

**h. Meetings & Site Inspections**

- Regular Site Visits were conducted by AHE and Inspection reports with observations were issued to the Contractor in accordance to the conformity of safe use of project highway.
- Site inspection carried out by the Resident Engineer, Maintenance Team Mr. Anjani Kumar and Sr. Bridge Engineer Mr. Rajiv Ranjan Verma along with Executive Engineer, P.W.D. Mr. Atul Kumar Sharma and Assistant Engineer, P.W.D. Mrs. Garima Srivastava on Dated 02<sup>nd</sup> August

2022 for Badaun-Bilsi-Bijnaour Road Project and their observations notified to the Contractor (GAWAR) vide letter No. Egis India/LKO/UPCRNDP/2022/1893 Dated 05.08.2022.

- Site Inspection carried out by the Assistant Engineer, P.W.D. Mrs. Garima Srivastav on occasion of Independence Day for flag hosting & Tree Plantation during Celebration of Azadi Ka Amrit Mahotsav on Dated 15.08.2022.
- Site Inspection of Maintenance Works by the Deputy Team Leader and Construction Safety Engineer on 16<sup>th</sup> and 17<sup>th</sup> August 2022 for Badaun-Bilsi-Bijnaour Road Project and their observations notified to the Contractor (GAWAR) vide letter No. Egis India/LKO/UPCRNDP/2022/1911 Dated 18.08.2022.

**i. Key Issues**

- 13 Nos. Bus Shelters location after finalization constructed by Contractor. Instructed Contractor to complete remaining 1 Nos. Bus Shelters painting ASAP.
- 02 Nos. Toilet Blocks at Truck Lay byes have not been constructed as local residents are objecting to the location shown on the approved drawings and therefore, the Contractor is discussing with the Authority representative for alternative locations.
- The 2 Nos. Completed Toilet Blocks must be fully functional and cleaned regularly by the Contractor.
- During O&M work Additional flagmen to be provided at work zone/diversion on live carriageway and all safety items such as water filled Plastic Barriers and advance signs to be maintained during the maintenance work and Contractor to take approval from AE for any lane closures of the live carriageway as per Clause 14.5 of the Contract Agreement.
- All Planted tree saplings to be watered regularly and the Contractor instructed to replace those which have died and balance saplings to be planted ASAP.
- Four Irrigation canal crossings by UP Irrigation Department with Bridge/Box Culverts have been completed and the pavement reinstated, however, concerns expressed of quality of work as per UPPWD standards. Maintenance of these sections will be the responsibilities of the Concerned Authority as the works were carried out by Irrigation Department Contractor after completion of the road by UPPWD Contractor.
- Only 11 No. of Table Top constructed by Contractor. Remaining Table top to be expedite for construction of Table top ASAP for safety of road users.
- Contractor has completed all CPR works but approval from the Authority is awaited regarding the CPR estimate approval request reminder has been given to Authority vide our letter no. Egis India/LKO/UPCRNDP/2022/1866 Dated 15.07.2022.

**j. Weather**

Weather Report for the reported period is shown in **Annexure-E**.

## **ENVIRONMENT, SOCIAL, HEALTH AND SAFETY**

## 22. ENVIRONMENT, SOCIAL, HEALTH AND SAFETY

### a. Introduction

This Environment-Social-Health-Safety Section of report of MPR is prepared for the all Four Civil Contract Packages of Phase-I roads. ESHS reporting is to ensure and appraise that the EMP implementation being carried out by the respective Contractors in accordance with their contract package requirements. It includes the EMP attributes monitored at Civil works Phase and O&M Phase of Contract packages.

To achieve the required environmental management standards, the Contractor of each project has been prepared the Environment and Social Management Plan (ESMP) which are approved by the Authority Engineer (AE)/ Construction Supervision Consultant (CSC) in accordance with the proposed mitigation measures recommended by the Project Management Consultant (PMC).

Phase-I Roads for development with Financial Assistance from the **World Bank**, International Bank for Reconstruction and Development (IBRD) is as per table below:

UPG-01 (Hamirpur-Rath)	SH-42	72.785km	262.39Cr	EPC Contract	O&M Phase
UPG-02 (Garautha-Chirgaon)	SH-42	49.145km	189.99Cr	Item Rate Contract	O&M Phase
UPG-03 (Gola-Shahjahanpur)	SH-93	57.535km	356.90Cr	EPC Contract	O&M Phase
UPG-04 (Badaun-Bilsi-Bijnaour)	SH-51	79.125km	334.00Cr	EPC Contract	O&M Phase

### b. ESHS Issues and Corrective Actions Taken

The ESHS issues of respective project sites has been monitored during the current month and presented in compiled environmental matrix:

#### i. Essential Project Insurances

Brief Status of essential Insurances is depicted below in Table-B.

Package	Table B -Status of Insurance Coverage					
	Employees Compensation (WC) Policy		Contractor's All Risk (CAR) Policy.		Public (3rd Party) liability Insurance	
	Insurer	Valid	Insurer	Valid	Insurer	Valid
UPG-01	IFFCO-TOKIO GENERAL INSURANCE CO.LTD	03-06-22 (Expired)	IFFCO-TOKIO GENERAL INSURANCE CO.LTD	11-07-26 Extended up to O&M Period	IFFCO-TOKIO GENERAL INSURANCE CO.LTD/32123941	11-07-26 Extended up to O&M Period
UPG-02	GO DIGIT GENERAL INSURANCE LTD.	21-08-23 (Renewed)	The New India Insurance Co. Ltd.	01-11-21 (Expired – DLP Over)	The New India Insurance Co. Ltd.	01-11-21 (Expired – DLP Over)
UPG-03	FUTURE GENERAL INDIA INSURANCE COMPANY LIMITED	03-04-23 (Renewed)	The New India Assurance Co. Ltd.	10-05-22 (Renewed) + 60months O&M Period	The New India Assurance Co. Ltd.	10-05-22 (Renewed) + 60months O&M Period

UPG-04	LIBERTY GENERAL INSURANCE LTD.	18-11-22 (Renewed)	ICICI Lombard General Insurance Company Ltd.	03-02-22 (Renewed) + 60months O&M Period	ICICI Lombard General Insurance Company Ltd.	03-02-22 (Renewed) + 60months O&M Period
--------	---	-----------------------	---	---	--	---

**Note:** UPG-01 the schedule and term of Contractor's CAR Policy under sub-clause C006 the O&M Period is covered.

UPG-02 WC Policy renewed; as per CA the CAR Policy was maintained up to DLP which is completed on 01-11-21 (extended 31-12-2021).

UPG-03 Renewal/ Extended copy of WC Policy & CAR Policy including DLP period is received;

UPG-04 Renewal/ Extended Copy of WC Policy & CAR Policy including DLP period is Received;

## ii. Borrow Areas

**SEIAA Permit for Borrow Area Operation** is exempted by the both MoEFCC Notification No. S.O.1224(E) dated 28<sup>th</sup> March, 2020 and State Govt. Order No.445/81-7-2020-39(Parya)/2014 T.C-1 dated 01-05-2020 for the Extraction or sourcing or borrowing of ordinary earth for the linear projects such as roads, pipelines etc. Brief status of Borrow Pits shown below:

<b>Table-C: Summary of the Selected Borrow Areas of the Contractors w.r.t EMAP.</b>									
Contract Package	Total No. of Borrow Areas Identified	No. of Borrow Areas approved w.r.t. EMP	No. of Borrow Areas				Rehabilitated	Balance for Rehabilitation	DC's Permission for borrowed Qty.
			Exhausted	Ongoing	Yet to be started	Qty. still Balance for use			
UPG-01	36	33	33	0	0	0	33	NIL	33
UPG-02	47	38	38	0	0	0	38	NIL	38
UPG-03	45	38	38	0	0	0	38	NIL	38
UPG-04	45	36	30	0	0	1	30	NIL	31
<b>Total</b>	<b>173</b>	<b>145</b>	<b>139</b>	<b>0</b>	<b>0</b>	<b>1</b>	<b>139</b>	<b>0</b>	<b>140</b>

**Note:**

**UPG-01,UPG-02, UPG-03& UPG-04:** Contractors have submitted the NOC for all the exhausted borrow pits.

**UPG-04:** 1 BA is kept for O&M period.

**iii. Status of O&M Phase ESMP Issues along with updated status is as below:**
**1. ESHS Cell/ Staff:**

<b>Table D: ENVIRONMENT MANAGEMENT SYSTEM CELL</b>					
<b>ORGANISATION</b>		<b>UPG-01</b>	<b>UPG-02</b>	<b>UPG-03</b>	<b>UPG-04</b>
(i)	Environment Cell (Employer)	MR. MUNNI LAL VERMA (Environment & Social Specialist - Executive Engineer; Mob.No.+91 9450577618) Dr. SEEMA SRIVASTAVA (Independent Consultant - Environment; Mob. No.+91 8887896070) Mr. P.N.ROY (Independent Consultant - Social; Mob. No.+91 9779117558)			
(ii)	Supervision Consultant (PMC/AE) at Team Leader Office	Mr. DEVBRAT SINGH (Environment Specialist - Mobilized on 13th April 2019; Mobile No.+91 9900034246; Mail ID: devbrat.s@egis-india.com)			

**2. Tree/ Avenue Plantation**

Tree plantation work was completed in all the EPC Contract Packages (except UPG-04) as the number of saplings prescribed in CA-Schedule-B sl.no.11. The Contractor has been advised for providing the Tree Guards in conformity of IRC-SP-21; commenced the plantation activities for replacement of dead plants and planting the remaining Trees; The status of proposed compensatory plantation are as below:

<b>Table-E: Tree/ Avenue Plantation Status (In Numbers)</b>					
<b>Package</b>	<b>No of Trees Cut</b>	<b>Trees as per CA</b>	<b>Length in Km</b>	<b>Completed</b>	<b>Balance</b>
UPG-01	54436	16952	26.354	16952	0
UPG-02	2456	4912	Forest Dept.	300	4612
UPG-03	6219	10578	14.37	10578	0
UPG-04	11079	31334	21.793	18484	12850
<b>TOTAL</b>	<b>74190</b>	<b>63776</b>	<b>62.517</b>	<b>46314</b>	<b>17462</b>
UPG-01: 8476 Trees and 45960 saplings were cut; UPG-02: Plantation work taken-up by Forest Department approx-300 saplings planted; UPG-03: Plantation works completed; UPG-04: In 4-lane section 850m length proposed for Shrub Plantation; (Ref. Egis India/LKO/UPCRNDP/2021/1489 Dt.30-10-2021); Plantation between Ch.107+200 to 137+525 could not be completed due to garbage dumped within Project ROW by local Municipal/Village Authority; a meeting between UPPWD & Municipal/ Local Administrative Authority is scheduled to resolve the issue urgently.					

**UPG-01 Hamirpur-Rath** The Replacement and plantation of deed plants has been taken-up by the Contractor during the current coming monsoon. **UPG-02** Compensatory Afforestation work to be taken-up by the Forest Dept.- Plantation yet to be started. **UPG-03 Gola-Shahjahanpur:** 5000 additional Tree plantation/ Saplings plantation taken-up during coming monsoon. **UPG-04** Remaining Tree plantation/ Saplings including replacement of deed plants to be taken-up, instruction issued as monsoon reason is on pick.

### 3. Rainwater Harvesting

RWH work is completed however all the Contractors instructed to maintain the earthen Toe drain & ROW cleaning for RWH to function efficiently.

<b>Table-F: Rain Water Harvesting Structures Status</b>			
<b>Package</b>	<b>RWH Progress Status (In Numbers)</b>		
	<b>Approved</b>	<b>Completed</b>	<b>Performance Verified</b>
UPG-01 Hamirpur-Rath	42	42	NIL
UPG-02 Garautha-Chirgaon	25	25	25
UPG-03 Gola-Shahjahanpur	89	89	NIL
UPG-04 Badaun-Bilsi-Bijnaour	112	112	NIL
<b>Total</b>	<b>382/268</b>	<b>268</b>	<b>25</b>
Note: The performance of Rainwater Harvesting is being monitored during the Monsoon.			

### 4. Environmental Enhancement

**UPG-01** Enhancement Work **completed** at all three locations.

**UPG-02** Both environmental enhancement site works are **completed**.

**UPG-03** Construction of bathing Ghat at Pond – **Completed** except site cleaning work.

**UPG-04** Enhancement at Dehpa Temple – New Hawankund – **completed**; Existing Temple enha. (wall& Slab & 1 Chabutra-Completed); Construction of bathing Ghat at Pond – **Completed**;

<b>Package</b>	<b>Table-G: Status of Environmental Enhancement in Numbers</b>							
	<b>Numbers</b>	<b>Chainage</b>	<b>Side</b>	<b>Existing Structure</b>	<b>Trees with Guard</b>	<b>Bench</b>	<b>Bathing Ghat</b>	<b>Status</b>
UPG-01	3	5+300	LHS	Temple	10	NIL	NIL	Completed at Ch.74+623
		5+800	RHS	Pond	15	NIL	NIL	Completed At Ch.9+800
		7+700	RHS	Temple	25	4	NIL	Completed
UPG-02	2	123+000	LHS	Temple	4	3	NIL	Completed
		165+000	LHS	Temple	4	4	NIL	Completed
UPG-03	3	9+300	RHS	School	16	NIL	NIL	Completed
		28+000	LHS	Pond	NIL	4	1	Completed
		52+000	LHS	School	15	NIL	NIL	Completed
UPG-04	2	61+500	LHS	Pond	NIL	4	1	Completed
		103+300	LHS	Temple	NIL	0	NIL	Completed
<b>Total</b>	<b>10</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>89</b>	<b>19</b>	<b>2</b>	

**Note:** UPG-01: Proposed CA Site was shifted in consultation with PAP and Client i.e. 5+300 to 74+623; 5+800 to 9+800; 7+700 – No change (Ref.GHV letter no.810 dt.16-04-2021)

## 5. Other Construction Work Sites Related Issues:

**UPG-01: Provisional Completion Certificate (PCC):** “The Engineer” has issued the PCC with effect from 12<sup>th</sup> July-2021 and further Final Completion Certificate was issued on 12<sup>th</sup> August 2021; The Project is under Operation and Maintenance Phase. The O&M Phase activities are being monitor as per Contractor’s Proposed O&M manual and Contractor ESMP Provisions.

- (i) **O&M Manual:** Contractor has submitted revised O&M Manual vide letter no. GHV/Site/SH-42/Rath/801 Dated- 01<sup>st</sup> April-2021 which is reviewed and approved as the Contractor has incorporated the EMP works and procedure of maintenance during O&M period (Ref. EGIS/1272 dt.20/04/2021)) – No Issue.

**UPG-02:** Project works are completed in all respect. Final Completion Certificate issued to the Contractor with effect 31<sup>st</sup> October, 2020; O&M Period is started from 01<sup>st</sup> November, 2020.

- (i) The Activities notified to the Contractor was not completed hence DLP period recommended to extend up to 31<sup>st</sup> Decemeber 2021 – Works were completed in Dec-21  
(ii) Avenue Tree Plantation shall be initiated by the Forest Department in consultation with Client/PWD.

**UPG-03:** DFO South Kheri demanded the provisions of 3 (Ch.12+870, Ch.13+546 & Ch.15+205, – Wild Animal /Cattle Underpass in the Reserve Forest Area Sections (Ch.12+000 to Ch.13+800 & Ch.14+680 to Ch.16+065); In principal the Authority has granted permission vide letter ref. no.95/800-6/UPCRNDP/WBYC/19 dated.17/01/2020.CUPworks are completed at all 3 locations except the chain-linked fencing along the forest boundary. The Draft Report on provisions of Wild Animal underpass at Reserve Forest Area has been prepared and submitted to Authority. The Completion Certificate is issued to the Contractor with effect from 15<sup>th</sup> March, 2022; O&M Period is started from 15<sup>th</sup> March, 2022.

**UPG-04:** Project works are completed in all respect. 12850 Compulsory plantation and construction of Project facility works (13 Bus Shelter + 2 Truck lay byes) shall be taken-up by the Contractor respectively after resolving the garbage dumping issue with the local municipal/panchayat authority and location disputes issues. The Completion Certificate is issued to the Contractor with effect from 10<sup>th</sup> January, 2022; O&M Period is started from 11<sup>th</sup> January, 2022.

### **Redevelopment of Exhausted Borrow Area:**

**UPG-03** the redevelopment works of exhausted borrow area - satisfactory.

**Removal of Construction Waste/ unserviceable Materials:** **UPG-01-** Final closure NOC for Contractor’s Camp at Ch.14+200 and Ch.57+000 is received. **UPG-02–** Final Closure NOC received. **UPG-03** Final closure NOC for Contractor’s Camp area (Ch.36+500 LHS) yet to be received **and UPG-04** Final Closure NOC for Contractor’s Camp Area (Ch.102+200) – yet to be received; Closure NOC for RMC Camp (Ch.95+760 RHS) - Received.

## c. Operation and Maintenance Stage Monitoring

The Authority Engineers’ (AE/PMC) Environmental Expert has inspected UPG-01, UPG-02, UPG-03 and UPG-04 during the O&M phase to ensure the compliance in conformity of Contract Environmental Management Plan (EMP).

The tree plantation status of EPC Contract monitored and suggested to the Contractors to timely taken-up replacement of dead plants for improved survival rate.

#### **d. Construction Site Management**

##### **i. Compliance Status of Environmental Safeguard**

The Environmental Safeguard implementation report received from the respective Project sites, Statutory Permit status is presented in table below:

**TABLE-H: STATUTORY PERMIT**

<b>S. No.</b>	<b>Key ESMP/Permit as per CA</b>	<b>Licensing Authority</b>	<b>UPG-01</b>	<b>UPG-02</b>	<b>UPG-03</b>	<b>UPG-04</b>
1	Approved Contractor Environmental & Social Management Plan (C-ESMP)	Contractor	Approved and uploaded on PWD Website	Approved and uploaded on PWD Website	Approved and uploaded on PWD Website	Approved and uploaded on PWD Website.
2	Operation and Maintenance (O&M) Manual	Contractor	Received & Approved by PMC	Received & Approved by PMC	Received & Approved by PMC	Received & Approved by PMC
3	Labour License	Labour Department	Available-Validity 03/09/2019 to 02/09/2022 (Renewed)	Available-Validity 26/04/2018 to 26/04/2022 (Renewal is in process)	Available-Validity 02/01/2020 to 10/11/2022 (Renewed)	Available-Validity 19/11/2019 to 17/11/2022 (Renewed)
4	Workmen Compensation Policy	Insurance Company	Validity till 03/06/2022 (Expired)	Available-Validity till 21/08/2023	Available-Validity till 03/04/2023	Available-Validity till 18/11/2022
5	Contractor All Risk Policy	Insurance Company	O&M Phase Covered	Available-Validity till 01/11/2021 (Validity was required till DLP)	Available-Validity till 10/05/2022 (Renewed) + 60 months for O&M Phase	Available-Validity till 03/02/2022 (Renewed) + 60 months for O&M Phase
6	PUC Certificates	State Transport Department	Available	Available	Available	Available
7	Borrow Area Permission	DC (Mining Department) and SEIAA	To date No BA for O&M Phase	To date No BA for O&M Phase	To date No BA for O&M Phase	To date No BA for O&M Phase
8	Signing Code of Conduct/Compliance of Covid-19 SOP	Contractor	Signed/Complied	Signed/Complied	Signed/Complied	Signed/Complied

### 23. CONSTRUCTION SAFETY MONITORING AND COMPLIANCE REPORT

S.No.	REQUIRED DATA		UPG-01	UPG -02	UPG-03	UPG-04	TOTAL
	Description	Unit	Month of August, 22	Month of August, 22	Month of August, 22	Month of August, 22	
SAFE MAN-HOURS ACHIEVE STATUS							
1	Average No. of Employees / Day Deployed at Project site (Skilled & Unskilled)	Nos.	6	5	26	15	52
2	Man-hours worked / Day (as above)	Hrs.	48	40	208	120	416
3	Man-hours worked during this month (Excluding Sunday & Holiday)	Hrs.	1200	1000	5408	3240	10848
PROJECT CRASH DATA REPORT							
1	First Aid Incidents	Nos.	0	0	0	0	0
2	Category (a) Incident: Involving Project Person or Project Machinery						
a	Fatal Incidents occurred at construction zone involving Project person/machinery	Nos	0	0	0	0	0
b	Major Injury	Nos	0	0	0	0	0
c	Minor Injury	Nos	0	0	0	0	0
d	Number of Near misses/ dangerous occurrences (including Property damage)	Nos	0	0	0	0	0
3	Category (b) Incident: Involving Public / Road Users adjacent to Work zones						
a	Fatal Incidents occurred at construction zone involving public	Nos	0	0	0	0	0
b	Major Injury	Nos	0	0	0	0	0
c	Minor Injury	Nos	0	0	0	0	0
d	Number of Near misses/ dangerous occurrences (including Property damage)	Nos	0	0	0	0	0
4	Category (c) Incident: Involving Public / Road Users beyond Work zones						
a	Fatal Incidents occurred at non-construction zone involving Public	Nos	2	0	3	0	5
b	Major Injury	Nos	0	0	0	6	6
c	Minor Injury(Road Incident Data )	Nos	0	0	0	0	0
d	Number of Near misses/ dangerous occurrences (including Property damage)	Nos	0	0	0	0	0

PROJECT ROAD SAFETY IMPLEMENTATION STATUS							
1	Road safety education and training	Nos	0	0	0	0	0
2	Percentage of compliance to unsafe acts & unsafe conditions	Nos	100%	100%	100%	100%	-
3	Number of Mock drill conducted	Nos	0	0	0	0	0
4	Awareness program conducted (Award / Reward to Worker / Engineers)	Nos	0	0	0	0	0
5	General Health checkup	Nos	0	0	0	0	0
<b>Note:- All data as provided by the Contractor and verified by AE's Field Staff. UPG-01 and UPG-02 Project Completed; O&amp;M Period is Under Progress.</b>							

**a. Road Safety Project Implementation Status**

ROAD SAFETY IMPLEMENTATION STATUS				
Vision Plans to Minimize Accidents				
S.N.	Project Name	Plans Description	Contractors Submission Date/ Letter No	AE's Approval Date and Letter No
1	UPG-01 HR-SH-42	Traffic Safety Management Plan (Rev-01)	GHV/Site/SH-42/Rath/197 Dated 14.10.2019	Egis India/RE-UPG-01/UPCRNDP/120/2019 Dated 04.12.2019
2	UPG-03 GSP-SH-93	Traffic Safety Management Plan (Rev-01)	APCO/Site/SH-93/GSP/ Letter No.59 dated 19.11.2019	Egis India/RE-UPG-03/UPCRNDP/ Approval Letter No. 33 dated 20.11.2019
3	UPG-03 GSP-SH-93	Diversion Plan for the Construction zone of project Highway. (Rev-00)	APCO/Site/SH-93/GSP/ Letter No.51 dated 06.11.2019	Egis India/RE-UPG-03/UPCRNDP/ Revision Letter No. 19 dated 13.11.2019
4	UPG-03 GSP-SH-93	Diversion Plan for the Construction zone of project Highway.(Rev-01)	APCO/Site/SH-93/GSP/ Letter No.58 dated 19.11.2019	Egis India/RE-UPG-03/UPCRNDP/ Approval Letter No. 32 dated 20.11.2019
5	UPG-04 BBB SH-51	Traffic Safety Management Plan	GCL/CAMP/SH-51/BBB/2020/131	Egis India/REUPG-04/UPCRNDP/087/2020 on 22.02.20
6	UPG-04 BBB SH-51	Diversion Plan for the Construction zone of project Highway.	GCL/Camp/SH-51/BBB/2020/399	Approved
7	UPG-02 G-C SH-42	Project Completed: Traffic Safety and Control Plan included in "Operation and Maintenance" Manual	O&M - NKC/Site/2020-21/GC/892 dated. 27-07-2020	Egis India/LKO/UPCRNDP/2020/934 dated 29.07.2020

CERTIFICATION & IMPLEMENTATION OF ISO STANDARDS				
1	UPG-01 HR-SH-42	ISO 14001 & ISO 45001	GHV/Site/SH-42/Rath/559 Dated 05-10-2020	ISO 14001 and ISO 45001 Valid till 07/11/2021
2	UPG-03 GSP-SH-93	ISO 14001 & ISO 45001	APCO/WB-UPPWD/EGIS/ST/525 Dated 13-06-2021	ISO 14001 Valid till - 27/08/2023 and ISO 45001 Valid till 29/03/2024
3	UPG-04 BBB SH-51	ISO 14001 & ISO 45001	GCL/Camp/SH-51/BBB/2021/518 Dated 12-02-2021	ISO 14001 Valid till - 10/02/2024 and ISO 45001 Valid till 10/02/2024
4	UPG-02 G-C SH-42	Project Completed -Not Applicable	NIL	NIL
CURRENT MONTH AE'S OBSERVATIONS & COMPLIANCE STATUS				
Before Executing any Activity, Safety Representative of AE (Egis) and concerned Field Engineer go through the RFI and Site Safety Arrangement as per provided Check list. If found satisfactory, Contractor permitted to proceed with the works. If not (RFI hold/rejected), and contractor informed to implement the safety in conformity of required Safety standards, which are then re- inspected prior to starting the works.				
ROAD SAFETY EDUCATION & TRAINING FOR ALL PROJECT EMPLOYEES				
Sl. No	Project Name	Description of program	Training provided by	No. of Person
1	UPG-01-HR-SH-42	Safety Induction (First-aid, Use the PPE's, & Working at heights)		0
2	UPG-01-HR-SH-42	Use the PPE's		0
3	UPG-01-HR-SH-42	Tool box talk		0
4	UPG-01-HR-SH-42	First-aid Training		0
5	UPG-01-HR-SH-42	Fire Extinguisher Inspection & Training		0
6	UPG-01-HR-SH-42	Vehicle Inspection & Training		0
S.No.	Project Name	Description of Program	Training provided by	No. of Person
1	UPG-02 G-C SH-42	Project Completed: Training on "How safely working on live road"		0
S.No	Project Name	Description of program	Training provided by	No. of Person
1	UPG-03 GSP-SH-93	NIL		
Sl. No	Project Name	Description of program	Training provided by	No. of Person
1	UPG-04 B-B-B SH-51	NIL		
ROAD SAFETY INSPECTION BY AE's HSE TO PROJECT WORKING SITE				
S.No.	Project Name	Description of Program	Training provided by	Condition
1	UPG-01-HR-SH-42	Plant & Equipment Inspection Done	0	0
2	UPG-01-HR-SH-42	Site SHE Inspection	0	0

3	UPG-01-HR-SH-42	Electrical Inspection	0	0
4	UPG-01-HR-SH-42	Work at Height Inspection	0	0
Sl. No	Project Name	Description of program	Training provided by	Condition
1	UPG-02 G-C SH-42	Project Completed: Inspection of all work site done by UPG-01 Staff	0	0
Sl. No	Project Name	Description of program	Training provided by	No. of Person
1	UPG-03 GSP-SH-93	Road Safety Awareness Training and use of the PPE's	0	0
2	UPG-03 GSP-SH-93	Oath ceremony, Road Safety Awareness Training and Pamphlet Distribution	0	0
3	UPG-03 GSP-SH-93	Road Safety Awareness Training and use of the PPE's	0	0
4	UPG-03 GSP-SH-93	Oath ceremony, Road Safety Awareness Training and Pamphlet Distribution	0	0
5	UPG-03 GSP-SH-93	TBT, Covid-19 awareness and maintain housekeeping.	0	0
6	UPG-03 GSP-SH-93	TBT, Covid-19 awareness and maintain housekeeping.	0	0
7	UPG-03 GSP-SH-93	Road Safety Awareness Training and Working at height using the platform	0	0
8	UPG-03 GSP-SH-93	Road Safety Awareness Training and using the PPE during work at height.	0	0
Sl. No	Project Name	Description of program	Training provided by	Condition
1	UPG-04 B-B-B SH-51	Fire Extinguisher Inspection	0	0
2	UPG-04 B-B-B SH-51	Vehicle Inspection	0	0
3	UPG-04 B-B-B SH-51	Plant & Equipment Inspection Done	0	0
4	UPG-04 B-B-B SH-51	Electrical Inspection	0	0
5	UPG-04 B-B-B SH-51	Site SHE Inspection	0	0
6	UPG-04 B-B-B SH-51	Housekeeping Inspection	0	0
7	UPG-04 B-B-B SH-51	Plant & Equipment Inspection Done	0	0
8	UPG-04 B-B-B SH-51	Electrical Inspection	0	0
9	UPG-04 B-B-B SH-51	Site SHE Inspection	0	0
10	UPG-04 B-B-B SH-51	Work at Height Inspection	0	0
11	UPG-04 B-B-B SH-51	Fire Extinguisher Inspection	0	0

**b. Safety Equipment at Sites during O&M Period**

Safety Items Name	UPG-01	UPG-02	UPG-03	UPG-04
PVC Plastic Barriers	22	16	30	30
Safety Cones	15	40	50	35
Safety Sign Boards	4	2	10	2
Flagmen	2	2	2	2

**c. Record with Dates of Completed Road Safety Audits on Phase-I Roads**

Pkg. No.	Road Name	Physical Progress as on 30 March 2022	Contract Completion Date/ Actual Completion Date	1 <sup>st</sup> Road Safety Audit Date During Construction	2 <sup>nd</sup> Road Safety Audit Date During Construction	3 <sup>rd</sup> Road Safety Audit Date After Completion	Remarks
UPG-02	Garautha-Chirgaon Section of SH-42 from Km. 118.600 to Km 167.745, Package No. UPG-02	100%	14.01.2020 Actual completion on 31 <sup>st</sup> OCT 2020	Completed on 10.FEB 2020	Completed on 02 SEPT 2020	Completed 04 DEC 2020	Works delayed due to land acquisition additional works and COVID-19. All works completed by 31 <sup>st</sup> October 2020
UPG-01	Hamirpur - Rath Section of SH-42, from Km 2.065 to Km 74.255 Pkg. No. UPCRNDP/UPG/01/2018	100%	23.06.2021 Actual completion on 12 <sup>th</sup> AUG 2021	Completed on 23. SEPT 2020	Completed 24 FEB 2021	Completed on 25 <sup>th</sup> AUG 2021	COVID-19 delays estimate Extension of Time (EOT) of 3 months. All works Completed on 12 Aug 2021
UPG-03	Gola - Shahjahanpur Section of SH-93, from Km 1.280 to Km 58.580 Pkg. No. UPCRNDP/UPG/03/2018	100%	09.11.2021 Actual completion on 15 <sup>th</sup> MARCH 2022	Completed on 29. SEPT. 2020	Completed on 6 JULY 2021	Completed on 8 <sup>th</sup> APRIL 2022	1 <sup>st</sup> & 2 <sup>nd</sup> wave of COVID-19 delays Extension of Time (EOT) of 4 months. Completed on Date 15 <sup>th</sup> March 2022
UPG-04	Badaun-Bilsi-Bijnaour of SH-51, from Km 58.400 to Km 137.820 in the State of Uttar Pradesh (Pkg. ICB No. UPCRNDP/UPG/04/2018	100%	02.11.2021 Actual completion on 10 JAN 2022	Completed on 08. OCT. 2020	Completed on 8 APRIL 2021	Completed on 27 JAN 2022	COVID-19 delays estimate Extension of Time (EOT) of 2 months. Completed on Date 10 <sup>th</sup> Jan 2022

## **24. SOCIAL MONITORING AND COMPLIANCE REPORT**

### **INTRODUCTION**

The current report is the monthly Social Safeguard Monitoring Report prepared to ensure the comply with the implementation arrangements agreement between World Bank and UPPWD. The main objective of this report is to brief the Land Acquisition and resettlement implemented across all the packages during the construction period.

The resettlement activities were achieved in all Four Packages of Phase-I Roads.

- Only one namely UPG-03 was required land acquisition. In UPG-03 (Gola-Shahjahanpur) the land acquisition was impacted nearly 92 Title Holders (TH).
- The other packages UPG-01, UPG-02 & UPG-04 involve resettlement of Non-Title Holders only. The compensation of NTH Disbursement of Structures Compensation & R&R Assistance Squatters & Encroachers was 100% & for Kiosks also 100% was disbursed within targeted period of time for successful implementation of civil works.
- As per original calculations/estimates, 3.0375 Hectare land was required but as per the actual field condition revised land 2.781 ha was required in order to minimize negative impacts and revised nos. of TH was affected only 84 TH.
- All the resettlement planning documents related to above projects were disclosed.

### **Status of Social Safeguard (PHASE- I ROADS)**

S. No.	Roads	Length (km)	Total Cost of LA and R&R (INR Cr.)	RAP Implementation on Phase-I Roads					
				Approve of Micro plans	Disbursement of Compensation & R&R Assistance	Distribution of Identity Cards	CPRs Relocation	Income Restoration Activities	Status of GRC
1	UPG-01: Hamirpur-Rath	72.785	2.120	Completed	Completed	Completed	Completed	Completed	Resolved
2	UPG-02: Garautha-Chirgaon	49.145	1.630	Completed	Completed	Completed	Completed	Completed	Resolved
3	UPG-03: Gola-Shahjahanpur	57.535	4.546	Completed	Completed	Completed	Completed	Completed	Resolved
4	UPG-04: Badaun-Bilsi-Bijnaour	79.125	0.226	Completed	Completed	Completed	Completed	Completed	Resolved
<b>TOTAL</b>		<b>258.59</b>	<b>8.522</b>						

## **RESETTLEMENT ACTION PLAN (RAP) IMPLEMENTATION BY NGO**

Non-Government Organization (NGO) M/s Study Point Samittee was initially appointed for implementation of RAP in Phase-I roads. However, on expiry of Contract Period the NGO's was not intended to extend his services. M/S Development Institute for Systems Alternatives (NGO) based in Lucknow was appointed to assist UPPWD to complete the remaining works of land acquisition and R&R activities. The services of above NGO awarded in under Contract No 123/1-13/UPCRNDP/CEEAP/2020 dated 21/10/2020 under IBRD- Loan No 8940-In.for implementation of Resettlement Action Plan (RAP).

All the micro plans were prepared and the Compensation of NTH Disbursement of Structures Compensation & R&R Assistance for Squatters & Encroachers is 100% & for Kiosks also 100% was disbursed.

## **STATUS OF CPRS**

It is communicated to the UPPWD, PMC, Contractor and NGO that total 43 CPRs for which the consent as well as site has already been identified, Design-drawing and construction plan with minor corrections are approved and Construction Works Completed and all CPRs are relocated.

## **TRAINING AND SUPPORT FOR INCOME RESTORATION**

The training programme was organized by the NGO in order to motivate and create interest among the PAPs to adopt Tool & Machinery trade as income generating livelihood and also to encourage the next future employment. The income restoration activities are completed.

## **CONCLUSION**

This was achieved through assessment of compliance with domestic policies, legislations and procedures as well as World Bank Safeguard Policy objectives. Generally, the implementation of the Resettlement Action Plan (RAP) was complied with the foregoing requirements.

With regards to the socio-economic status of the PAPs before and after RAP implementation, the study has concluded that there was no serious impacts on the livelihood structure of PAPs and access to land, livestock or sources of income. Similarly, patterns of social interactions remained intact. RAP implementation did not have any livelihood impacts as there was no loss of access to different public services such as schools, health facilities, sewage lines, water reticulation points, loss of access to markets, loss of access to suppliers or even support networks.

**COMPONENT PART- C**

**PROJECT MANAGEMENT SERVICES (TIME BASED)**

## **25. PART-C COMPONENT**

### **a. OVERALL PROGRESS OF UPCRNDP – PMC's SCOPE**

<b>CLAUSE 3.8</b>	<b>COMPONENT</b>	<b>PROGRESS STATUS</b>
a	Prepare overall plan and schedule for Project	Overall Plan for project was prepared and shared with PWD at the time signing of the Contract
b	Assist PWD in preparation of the overall project implementation program	We have been closely working with PWD in implementing overall program for completing the Project.
c	Co-ordination between Project's component to incorporate findings/ recommendations in design & implementation	Being implemented – iRAP survey data incorporated in Phase-I DPR; Independent RSA findings implemented in UPG-02; ECORYS GAC recommendations incorporated in Phase-II design
d	Monitor actual Physical Progress and costs against plans & budget and prepare QPR	Being Implemented
e	Monitor the progress and quality of construction/ maintenance works for compliance with the contractual provisions.	Being Implemented
f	Safety Audit – 2 construction stage & 1 post construction stage	Completed - all 3 safety audit for UPG-2 Garautha-Chirgaon & UPG-01( Hamirpur-Rath), UPG-03 (Gola-Shahjahanpur) & UPG-04 (Badaun-Bilsi-Bijnaour); Compliance report from the Contractors has been received and sent to the UPPWD.
g	Assess the achievement of Project Development Objectives through monitoring of result framework / indicators agreed between Bank and GoUP.	Being implemented and monitored in QPR
h	Prepare RFP/ ToRs for any additional consultancy	We have assisted in preparing RFP/ToRs for appointing Independent consultants
i	Prepare Mid-Term Review Report of the Project in agreed format.	Mid-Term Review Report has been prepared and submitted to UPPWD
j	Contract Analysis and make recommendations	Being Implemented
k	Training to PWD staff on Road Safety, Quality Control and Contract.	Road Safety and Quality training provided and Contract Administration Delayed due to Covid-19; will be provided as per PWD convenience.
l	Monitor Project costs and provide updated forecast of costs in QPR	Being Implemented
m	Develop a Quality Management System	Quality Management Procedure Manual shared with PWD for phase –I. Manuals for Phase-II under preparation expected to be submitted by Mid November 2022
n	Support the development of PWD's – RAMS, Preparation of Bid Documents, Data Collection Services from other sources.	Being Implemented

o	Project Risk Management – identification, analysis and Mitigation Plan	Risk Management status updated in the report.
p	Training to stakeholders on PMIS	Being Provided;
q	Operational and maintenance support for PMIS	Being Implemented
r	Organize various stakeholder workshops – Project launch; Mid-Term etc.	Project Launch Workshop was planned around mid-March 2020 but due to Covid-19 Cancelled; Mid-Term & other workshop will be implemented in consultation with PWD & WB.
s	Participation in various discussions/ meetings/ missions called upon by WB	Being Implemented

**Risk Management Status as on 31.08.2022 is tabulated as follows:**

**(a) Project Risk Management During Preparation of DPR**

Sl. No.	Risk Title	Consequences/Impacts	Risk Owner	Risk Sev.	Risk Mitigation Plan
1	Alignment Confirmation	Time	UPPWD	M	UPPWD to confirm alignment of Road ASAP to start the process
2	Initial Report to highlight the constraints	Time	UPPWD	M	Meetings with different departments to be arranged to check the constraints
3	Forest - Identify Forest area and start process	Time/Cost	UPPWD/PMC	M	Forest land to be identified ASAP and start processing in order to take permission for land acquisition/tree cutting
4	Land Acquisition- Land owner process/Corresponding	Time/Cost	UPPWD/PMC	M	Land data should be submitted to local administration/demarcation of land/identification of land owner in coordination with Lekhpal/Tehsildar
5	Staff- Experienced staff for DPR	Time/Cost	PMC	H	Specialized staff to be deployed in the start to prepare good quality DPR
6	Program for DPR submission	Time	PMC	M	Submit program for DPR in details including environment and Social.
7	Regular staff visit with Client	Time	UPPWD/PMC	M	Design team to schedule a program for site visit to get the datas and record other Hindrances, Safety issues etc;
8	Use of Codes	Cost	PMC	M	Latest design codes to be used during the preparation of DPR
9	Procurement of Agencies	Time and Cost	UPPWD	M	Procure agencies within time for Survey, Land/Traffic/others related to project.

10	Comments from Client/Funding Agency/WB	Time and Cost	All	M	Early response to clients/WB comments and compliances within the time schedule
11	Force Majeure Event	Time/Cost	All	L	Very difficult to predict Pandemic, Earthquakes, Adverse weather (Storm/Flooding), Civil War/War/ Political unrest. Evaluate the cost and time afterward immediately

**(b) Project Risk Management during Maintenance Period of Completed Phase-I Roads**

Risk #	Risk #	Risk Title	Consequences/ Impacts	Risk Owner	Risk Sev.	Mitigation Plan/Action Taken
1	Technical	Maintenance Inspection Note issued to the Contractors with Time Period for Rectification.	Safety of Road User with deterioration of defects.	AE / Contractor	M	Authority Engineer to ensure the early joint inspection of roads and notify the defects to Contractor in 1st week of every month and follow up the defect rectification
2	Technical	Maintenance Program for Defects	Road users Travelling time, Safety impacted negatively.	Contractor	M	Contractor to Submit the Maintenance Program as per Clause 14.3 of Article 14 of Contract Agreement (CA) on every month/prior to start any Maintenance work on Live Carriageway
3	Safety During Maintenance Works on Live Carriageway	Submission of Traffic Diversion Plan for Lane Closure on live carriageway	Fatal Accident involving General public & Contractor's workers	Contractor	H	Contractor to Submit the Traffic Management Plan for Lane Closure as per Clause 14.5 of Article 14 of Contract Agreement with details of manpower and equipment availability and get approval from AE prior to start any work on the live carriageway. AE to check the safety equipment such as water filled plastic barrier, traffic cones, advance warning signs availability in contractor's Yard prior to approve the Diversion Plan for lane closure.
4	Technical	Delay in rectification of notified defects	Can cause Fatal/ Serious injury & defect can get worse and increased the risk of accident/breakdown of vehicle	Contractor	M	Contractor to rectify the defects as per notified time period as per Schedule-E of CA for smooth flow of Traffic. AE to take serious action/inform client for initiating notice as per clause 14.7 of EPC Mode Contract & clause 36.1 for BOQ Mode Contract and made deduction from the Monthly Maintenance Statement

5	Safety of Road Users and pedestrians	Public Vehicle Breakdown/Accident/Encroachment on shoulder and carriageway with storage of building materials.	Traffic Jam/Inconvenience to road user and Hazards can cause serious accident	Contractor	H	Contractor to be vigilant and operate 24x7 a patrolling vehicle inform all emergency authorities immediately & make arrangements to clear the highway with Hydra Crane.
6	Environment	Survival of Planted Trees (Non watering of Trees)	Plant will die/impact of air pollution/encroachment of ROW area reducing the environmental enhancement.	Contractor	M	Contractor to water the plant continue and protect from animals by providing Tree Guards and regular maintenance and monitoring of the survival planted trees. Contractor also to replace the dead plant with new.
7	Environment	Functioning of Rain Water Harvesting (RWH)	Wastage of water/ water will not percolate into the soil to raise water table	Contractor	M	Contractor to clean the weep holes of top slab of RWH and remove silt from the pit as per CA ensure the efficient functioning of RWH. Contractor/AE to monitor the maintenance regularly.
8	Insurance Policies	Various Insurance Policies as per Contract Agreement to be renewed before the Policy expiring date during the Maintenance period.	Compensation claims due to accidents and major failures of the completed road could be denied by the Contractor's insurers leading to claims against the Authority	Contractor	M	AE to check on regular basis on the Contractors all required Insurance Policies for validity and amounts insured and ensure that the Contractors is informed with warning to extend any policies near expiring and submit copies of the extended insurance policies to AE for approval confirmation
9		Submission of Compliance Report of Inspection Note Timely	Delay in recommendation of Payment to Contractor	Contractor	M	Contractors to rectify the defects noted time period in Schedule-E for EPC Contracts and submit the compliance report to AE as per Contract Agreement. Similarly for BOQ Contract as per the Table under Clause A-1.3.

**b. Status of Consultancy Services required and Mobilized under UPCRNDP**

SL No.	Description of Services	Methods of Selection	Review Type	Present Status	Name Of Consultant / Firm
1	Project Management Consultancy (PMC's)	QCBS	Prior	Contract awarded & commencement from <b>08 August, 2014</b>	M/s Egis India Pvt. Ltd
2	Independent Environmental and social review consultant.	QCBS	Prior	Contract awarded and commencement from <b>19 February , 2015</b>	M/s EQMS India Pvt. Ltd.
3	Providing NGO (firm) Services (for Facilitating Implementation of resettlement Action Plan) .	LCS	Prior	Contract awarded and commencement from <b>03 Feb, 2018. Now Demobilized.</b>	M/s Study Point Samiti
4	Gender Assessment and Preparation of Gender Action Plan.	QCBS	Post	Contract awarded and commencement from <b>18 July, 2019.</b>	M/s ECORYS INDIA Pvt. Ltd.
5	Individual Consultant (IC) for the Consultancy Services to support the Social component under Environment and Social Development Cell (ESDC).	ICS	Post	Contract awarded and commencement from <b>05 May, 2020.</b>	Mr. Prabhanjan Narayan Roy
6	Individual Consultant (IC) for the Consultancy Services to support the Environmental component under Environment and Social Development Cell (ESDC).	ICS	Post	Contract awarded and commencement from <b>06 May, 2020.</b>	Dr. Seema Srivastava
7	Phase-1 of NGO (firm) services to undertake balance activities.	SSS	Post	Contract awarded and commencement from <b>21 October, 2020.</b>	M/s Development Institute For Systems Alternatives.
8	Consultancy for Financial Management Firm.	QCBS	Post	Contract awarded and commencement from <b>18 January, 2021.</b>	M/s Asija & Associates LLP
9	Consultant firms for conducting Road User Satisfaction Surveys (Baseline).	QCBS	Post	Contract awarded and commencement from <b>18 January, 2021.</b>	M/s Marketing and Research Development Associates (MDRA)

<b>10</b>	<b>Consultancy Services for Independent Quality Auditor for UP Core Road Network Development Project proposed from World Bank Loan.</b>	<b>QCBS</b>	<b>Post</b>	Contract awarded and commencement from <b>18 January, 2021.</b>	<b>M/s TUV-SUB South Asia Private Limited</b>
<b>11</b>	<b>Phase-2 of NGO Services.</b>	<b>QCBS</b>	<b>Post</b>	Contract awarded and commencement from <b>28 April, 2022.</b>	<b>M/s SUGAM INTERNATIONAL SANSTHAN</b>
<b>12</b>	<b>Consultancy for Internal Auditor (Financial)</b>	<b>QCBS</b>	<b>Post</b>	Contract awarded on <b>26 April, 2022</b> and commencement from <b>24 May, 2022</b>	<b>M/s S.N. KAPUR AND ASSOCIATES</b>
<b>13</b>	<b>Consultancy Services for Road Asset Management System support to the UPPWD under Uttar Pradesh Core Road Network Development Program (UPCRNDP) (Individual).</b>	<b>QCBS</b>	<b>Post</b>	Contract awarded and commencement from <b>05 May, 2022.</b>	<b>Mr. Srinivas Rao Nayani</b>
<b>14</b>	<b>Phase-2 of Supervision Consultancy.</b>	<b>QCBS</b>	<b>Prior</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process.</b> # RFP issue to shortlisted firm on dated 09-Feb-2022 # Bid Received &amp; Technical Bid open on dated 25-March-2022. #TEC Evaluation Done on 23-April-2022 now Bids are under PSC &amp; WB Approval.</li> </ul>	
<b>15</b>	<b>PMC for Road Safety Activities to be implemented by UPPWD under UPCRNDP</b>	<b>QCBS</b>	<b>Prior</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process.</b> #RFP issued on 12 May 2022 &amp; #Prebid meeting on 27 May 2022 #Technical Bid open on dated 11 July 2022. #TEC meeting on 23-Aug-2022 and next TEC meeting reschedule for the month of September.</li> </ul>	

16	<b>External Evaluation Consultant for RAP implementation</b>	<b>QCBS</b>	<b>Post</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process</b></li> <li># <b>EOI was opened on 12 Jan, 2022.</b></li> <li># <b>EOI open on dated 12 Jan, 2022 &amp; EOI Evaluated by TEC on 5-6 Feb 2022.</b></li> <li># <b>Approved by PSC (Project Steering Committee) &amp; World Bank.</b></li> <li># <b>RFP issue to shortlisted firm on dated 04-April-2022</b></li> <li># <b>Bid Received &amp; Technical Bid open on dated 04-May-2022.</b></li> <li># <b>TEC Evaluation Done on 17-18-June-2022 now Bids are under PSC/WB Approval.</b></li> </ul>
17	<b>Consultant firms for conducting Road User Satisfaction Surveys (Baseline) for Phase-2 Roads.</b>	<b>QCBS</b>	<b>Post</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process</b></li> <li># <b>TOR under World Bank Approval.</b></li> </ul>
18	<b>Mid-term &amp; End-term evaluation of Road User Satisfaction Surveys for Phase-1 &amp; 2 Roads</b>	<b>QCBS</b>	<b>Post</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process</b></li> <li># <b>TOR in Progress.</b></li> </ul>
19	<b>Consultancy Services for Independent Quality Auditor for Phase-2 Roads UP Core Road Network Development Project proposed from World Bank Loan.</b>	<b>QCBS</b>	<b>Post</b>	<ul style="list-style-type: none"> <li>• <b>Procurement under process</b></li> <li># <b>TOR in Progress.</b></li> </ul>

**c. STATUS OF VARIOUS CIVIL WORKS (Procurement Status of Phase-II Roads)**

SL No.	Description	Methods of Selection	Review Type	Present Status
1	Up gradation & Maintenance of Rath-Garautha Section of SH-42 (Missing Link)	NCB	prior	<ul style="list-style-type: none"> <li>• RFB Published on Date 16-April-2022</li> <li>• Bid Received &amp; Technical Bid open on dated 31-May-2022.</li> <li>• TEC Evaluation Done on 17-18-June-2022 &amp; 23 Aug. 2022.</li> <li>• Technical Bids evaluation report sent to WB for approval on 24.08.2022</li> </ul>
2	Engineering Procurement and Construction Contract [EPCC] for Up gradation and Maintenance of Banshi-Mehandawal-Khalilabad Road (SH-88)	NCB	prior	<ul style="list-style-type: none"> <li>• RFB Published on Date 18-April-2022,</li> <li>• Bid Received &amp; Technical Bid open on dated 03-June-2022.</li> <li>• TEC Evaluation Done on 17-18-June-2022</li> <li>• Approval from WB on technical BER obtained on</li> <li>• Financial bid opened on 26.07.2022</li> <li>• TEC evaluated financial bid on 23.08.2022</li> <li>• Financial bid evaluation report sent to WB for approval on 24.08.2022</li> </ul>

3	Engineering Procurement and Construction Contract [EPCC] for Up gradation and Maintenance of Bahraich-Gonda-Faizabad Road (SH-30)	ICB	prior	<p>The Government of Uttar Pradesh has given administrative and financial approval to the project.</p> <ul style="list-style-type: none"> <li>RFP was published on E-Tender portal on 03.08.2022</li> <li>The last date of bid submission is 20.09.2022</li> <li>Pre proposal meeting was held on 26.08.2022 and NOC on minutes of pre proposal meeting from WB was obtained on 31.08.2022</li> </ul>
4	Engineering Procurement and Construction Contract [EPCC] for Up gradation and Maintenance of Hamidpur-Kuchesar Road (SH-100)	NCB	prior	<p>Estimate send to UP Government on dated 29.04.2022. Under administrative and financial approval of Government of Uttar Pradesh.</p> <ul style="list-style-type: none"> <li>The procurement plan was uploaded on STEP portal on dated 02.09.2022 and is under review from WB</li> </ul>
5	Engineering Procurement and Construction Contract [EPCC] for Up gradation and Maintenance of Garh-Syana-Bulandshehar Road (SH-65)	ICB	prior	<p>Estimate send to UP Government on dated 30.04.2022. Under administrative and financial approval of Government of Uttar Pradesh.</p> <ul style="list-style-type: none"> <li>The procurement plan was uploaded on STEP portal on dated 02.09.2022 and is under review from WB</li> </ul>
6	Engineering Procurement and Construction Contract [EPCC] for Up gradation and Maintenance of Moradabad-Haridwar-Dehradun Road (SH-49)	ICB	prior	<p>Estimate send to UP Government on dated 22.04.2022. Under administrative and financial approval of Government of Uttar Pradesh.</p> <ul style="list-style-type: none"> <li>The procurement plan was uploaded on STEP portal on dated 02.09.2022 and is under review from WB</li> </ul>

**\*ICB- International Competitive Bidding**

**\*NCB-National Competitive Bidding.**

**d. Financial Progress of Consultant (PART-C)**

Financial Expenditure of PMC Services up to August 2022

PART - C – Up to August 2022 (USD) - CLAIMED AMOUNT

SI No.	Description	Contract Amount	Variation	Cumulative up to Current Invoice	Balance
1	Remuneration for TL	\$11,24,640	\$12,25,501	\$9,42,711	\$2,82,790
<b>Gross Amount (Foreign Component)</b>		<b>\$11,24,640</b>	<b>\$12,25,501</b>	<b>\$9,42,711</b>	<b>\$2,82,790</b>
2	Escalation			\$66,951	
<b>Grand Total</b>		<b>11,24,640</b>	<b>12,25,501</b>	<b>\$10,09,662</b>	

PART - C - Up to August 2022 (INR) - CLAIMED AMOUNT

SI No.	Description	Contract Amount (INR)	Variation (INR)	Cumulative up to Current Invoice (INR)	Balance (INR)
1	Remuneration for Key Professionals	5,20,34,400	4,32,39,000	1,60,86,872	2,71,52,128
2	Reimbursable Expenses	1,85,52,152	3,08,96,321	2,16,13,412	92,82,909
<b>Total</b>		<b>7,05,86,552</b>	<b>7,41,35,321</b>	<b>3,77,00,284</b>	<b>3,64,35,037</b>
3	Escalation			50,97,812	
<b>Grand Total</b>		<b>7,05,86,552</b>	<b>7,41,35,321</b>	<b>4,27,98,096</b>	

**PART – B:**

**CONSTRUCTION SUPERVISION OF CIVIL WORKS**

**PHOTOGRAPHS**

**1) PHOTOGRAPHS OF PACKAGE –UPG/02 (GARAUTHA – CHIRGAON)**



Ch. 125+600 - Bushes Cutting work is in Progress



Ch. 131+730 - Tiles Repairing Work is in Progress



Ch. 118+845 - Damaged Hazard Sign Board Replaced



Ch. 129+800 - Weep holes Cleaning is in Progress



Tree Plantation on the occasion of 75<sup>th</sup> Anniversary of Independence Day during Azadi Ka Amrit Mahotsav



Ch. 130+550 - Drain Cover Replacing Work is in Progress

**2) PHOTOGRAPHS OF PACKAGE UPG/01 (HAMIRPUR-RATH)**



Weep holes Cleaning completed



Tree Plantation on the occasion of 75<sup>th</sup> Anniversary of Independence Day during Azadi Ka Amrit Mahotsav



Bushes Cutting work is in Progress



Ch. 53+000 to Ch. 54+000 - Tree Guard provided



Cleaning of Bus Shelter



Replacing of Sign Board

### 3) PHOTOGRAPHS OF PACKAGE –UPG/03 (GOLA-SHAHJAHANPUR)



Tree Plantation on the occasion of 75<sup>th</sup> Anniversary of Independence Day during Azadi Ka Amrit Mahotsav



Minor Bridge at Km. 7+163 - Drainage L Pipes provided



Bushes Cutting works is in Progress



Damaged Sign Board Replaced



Shoulder Repairing Works are in Progress



Bus Shelter Cleaning Work is in Progress

**4) PHOTOGRAPHS OF PACKAGE –UPG/04 (BADAUN-BILSI-BIJNAOUR)**



Drain weep holes cleaning is in progress



Ch. 87+300 - Construction of Table Top is in Progress



Damaged Sign Board Replaced



Bushes Cutting Work is in Progress



Tree Plantation done on the occasion of 75<sup>th</sup> Anniversary of Independence Day during Azadi Ka Amrit Mahotsav



Tree guard installation is in progress

**Enclosure-1**

**Summary of Team Leader Office  
Correspondences**

**Minutes of Meeting (MoM) Letters**

## Consultancy Services for Uttar Pradesh Core Road Network Development Program

### OUTGOING CORRESPONDANCES of TL OFFICE, LUCKNOW for the m/o AUGUST 2022

Sr.No.	Letter Date	Letter Reference No.	To	Subject	Incoming Letter Reference
1	01.08.2022	Egis India/LKO/UPCRNDP/2022/1886	CE,PWD,Lucknow	Compliances to World Bank Team Comments on DPR of Moradabad-Haridwar-Dehradoon (SH-49)	
2	01.08.2022	E-Mail	CE,PWD,Lucknow	Submission of Detailed Project Report of Bahraich-Gonda-Faizabad Road (SH-30) – <b>Final BID Document (Rev.8) Month August 2022</b>	
3	02.08.2022	Egis India/LKO/UPCRNDP/2022/1887	EE,PWD,Jhansi	Regarding Damaging the Road by Sand Mining Agency on Hamirpur-Rath Project SH-42	GHV letter No. 1887 Dated 02.08.2022
4	02.08.2022	E_MAIL	CE,PWD,Lucknow	<b>NOC from the World Bank for ICB SH-30 bid document of SH-30</b>	
5	02.08.2022	E_MAIL	CE,PWD,Lucknow	DPR Volume VII - Bid Document (Rev.1) of Hamirpur-Kuchesar Road (SH-100)	
6	03.08.2022	Egis India/LKO/UPCRNDP/2022/1888	CE,PWD,Lucknow	CVs for the DAAB Members for Moradabad-Haridwar-Dehradoon (SH-49) and Garah-Sayana-Bulandshahar (SH-65)	
7	04.08.2022	Egis India/LKO/UPCRNDP/2022/1889	GHV/APCO/GAWAR	Tree Plantation/ Greenbelt Development of CA Schedule-D Appendix A-1 ESMP Table 1.3 Environmental Monitoring Plan	
8	04.08.2022	Egis India/LKO/UPCRNDP/2022/1890	CE,PWD,Lucknow	Reimbursement of GST against Invoice claimed for the month of May 2022 against Part-A (Phase-II Roads), Part-B & C of UPCRNDP (USD and INR Components)	
9	04.08.2022	Egis India/LKO/UPCRNDP/2022/1891	APCO	Site Inspection Report of Resident Engineer, Maintenance Team and Sr. Bridge Engineer Dated 01.08.2022 during the Maintenance Period	

10	04.08.2022	Egis India/LKO/UPCRNDP/2022/1892	APCO	Site Inspection of Principal Secretary regarding Tree Plantation Scheduled to be held on 10.08.2022	PWD letter No. 582 Dated 04.08.2022
11	05.08.2022	Egis India/LKO/UPCRNDP/2022/1893	GAWAR	Site Inspection Report of Resident Engineer, Maintenance Team and Sr. Bridge Engineer Dated 02.08.2022 during the Maintenance Period	
12	05.08.2022	Egis India/LKO/UPCRNDP/2022/1894	CE,PWD,Lucknow	Request for Approval of Cost Estimate for 11 Nos. Common Property Resource (CPR) Structures as per Article-09 of the Contract Agreement - (Reminder) for Badaun-Bilsi-Bijnaour Road Project	
13	05.08.2022	Egis India/LKO/UPCRNDP/2022/1895	BSNL	Payment of BSNL Outstanding Bill of INR 2093/- for Account No. 1022911678.	
14	05.08.2022	Egis India/LKO/UPCRNDP/2022/1896	GHV	Site Visit Program of Resident Engineer & Sr. Bridge Engineer on 08.08.2022 for Hamirpur-Rath Road Project	
15	05.08.2022	Egis India/LKO/UPCRNDP/2022/1897	NKC	Site Visit Program of Resident Engineer & Sr. Bridge Engineer on 09.08.2022 for Garautha-Chirgaon Road Project	
16	06.08.2022	Egis India/LKO/UPCRNDP/2022/1898	CE,PWD,Lucknow	Request to Release of Our Long Pending Payments – (Reminder)	
17	08.08.2022	Egis India/LKO/UPCRNDP/2022/1899	CE,PWD,Lucknow	Submission of USD Component Invoice No.95 for the month of July 2022	
18	08.08.2022	Egis India/LKO/UPCRNDP/2022/1900	CE,PWD,Lucknow	Submission of Part-B and Part-C INR Component Invoice No.101 for the month of July 2022	
19	08.08.2022	Egis India/LKO/UPCRNDP/2022/1901	CE,PWD,Lucknow	Site Visit Schedule of Acting Team Leader and Experts for August 2022	
20	09.08.2022	Egis India/LKO/UPCRNDP/2022/1902	APCO	Returning of Final Payment Statement (Interim Payment Application No. 17) for Stage Payment No. 16 due to Non Submission of Rate Analysis of Dense Bituminous Macadam (DBM I&II) Mix Design (Job Mix Formula-JMF) Grade-I & Grade-II & Compare with Reclaimed Bituminous Mix Design (RBM)	APCO letter No. 767 Dated 15.07.2022

21	09.08.2022	Egis India/LKO/UPCRNDP/2022/1903	GHV/APCO/GAWAR	Regarding Road Roughness (Bump Integrator) Test	
22	09.08.2022	Egis India/LKO/UPCRNDP/2022/1904	SE,PWD,Lucknow	(Online Forest Proposal No. FP/UP/ROAD/147236/2021) Regarding Submission of double degraded Forest land details for Compensatory Afforestation of Bahraich-Gonda-Faizabad (SH-30)	
23	09.08.2022	Egis India/LKO/UPCRNDP/2022/1905	GHV	Regarding Repairing of PQC Cracks	
24	09.08.2022	Egis India/LKO/UPCRNDP/2022/1906	GHV	Site Visit & Inspection Report of the Resident Engineer, Maintenance Team and Sr. Bridge Engineer on Dated 8th August 2022 for Hamirpur-Rath Road (SH-42)	
25	11.08.2022	Egis India/LKO/UPCRNDP/2022/1907	GAWAR	Site Visit of Deputy Team Leader and Construction Safety Engineer on 16th and 17th August 2022	
26	11.08.2022	Egis India/LKO/UPCRNDP/2022/1908	GAWAR	Regarding Construction of Table Top in place of Dismantled Speed Breakers	PWD letter No. 650 Dated 06.08.2022
27	12.08.2022	E-Mail	CE,PWD,Lucknow	Compliances of World Bank Comments Dated 08.08.2022 on DPR of Garah-Sayana-Bulandshahar Road (SH-65) and Hamidpur-Kuchesar Road (SH-100)	
28	13.08.2022	Egis India/LKO/UPCRNDP/2022/1909	GHV-NKC-APCO-GAWAR	To Implement the Program of Flag Hosting and Planting Trees during the Celebration of Amarat Mahotsav of Independence Day from 11.8.2022 to 17.08.2022	PWD letter No. 603 Dated 11.08.2022
29	16.08.2022	Egis India/LKO/UPCRNDP/2022/1910	CE,PWD,Lucknow	Consolidated Monthly Progress (Operation & Maintenance) Report (CMPR) No. 37 for the month of July 2022	
30	18.08.2022	Egis India/LKO/UPCRNDP/2022/1911	GAWAR	Site Inspection Report of Deputy Team Leader Dated 16th and 17th August 2022 during Operation and Maintenance (O&M) Period	

31	18.08.2022	Egis India/LKO/UPCRNDP/2022/1912	GAWAR	Non Submission of Rate Analysis of Dense Bituminous Macadam (DBM I&II) Mix Design (Job Mix Formula-JMF) Grade-I & Grade-II & Compare with Reclaimed Bituminous Mix Design (RBM) - <b><u>REMINDER-5</u></b>	
32	22.08.2022	Egis India/LKO/UPCRNDP/2022/1913	SE,PWD,Kanpur	Recommendation of Monthly Maintenance Statement No. 07 (21st March, 2022 to 30th June, 2022) (IPC-07) as per Special Conditions of Contract (SCC) Clause 42.7 (a) & 47 of SCC of Contract Agreement.	NKC letter No. 192 Dated 08.08.2022
33	22.08.2022	Egis India/LKO/UPCRNDP/2022/1914	SE,PWD,Kanpur	Recommendation of Monthly Maintenance Statement No. 08 (01st July, 2022 to 31st July, 2022) (IPC-08) as per Special Conditions of Contract (SCC) Clause 42.7 (a) & 47 of SCC of Contract Agreement.	NKC letter No. 193 Dated 08.08.2022
34	24.08.2022	Egis India/LKO/UPCRNDP/2022/1915	CE,PWD,Lucknow	Approval of CV Submission of Sub-professional Staff for the Position of Assistant Highway Engineer Mr. Rajeev Ranjan	PWD letter No. 1459 Dated 12.07.2022
35	25.08.2022	Egis India/LKO/UPCRNDP/2022/1916	NKC/APCO/GAWAR	To Implement the Program of Flag Hosting and Planting Trees during the Celebration of Amarat Mahotsav of Independence Day from 11.8.2022 to 17.08.2022 - <b><u>REMINDER</u></b>	
36	25.08.2022	Egis India/LKO/UPCRNDP/2022/1917	GAWAR	Regarding Construction of Table Top in place of Dismantled Speed Breakers - <b><u>REMINDER</u></b>	
37	26.08.2022	Egis India/LKO/UPCRNDP/2022/1918	CE,PWD,Lucknow	Approval of Replacement CVs of Mr. Jagdish Prasad for Sr. Bridge Design Engineer (Intermittent) and Mr. Satya Vrat Pandey for Social Development Specialist(Intermittent) for Part-C Services - <b><u>REMINDER</u></b>	
38	26.08.2022	Egis India/LKO/UPCRNDP/2022/1919	SE,PWD,Lucknow	(Online Forest Proposal No. FP/UP/ROAD/147236/2021) Regarding Re-submission of double degraded Forest land details for Compensatory Afforestation (Bahraich - Gonda SH-30)	
39	26.08.2022	Egis India/LKO/UPCRNDP/2022/1920	SE,PWD,Kanpur	(Online Forest Proposal No.- FP/UP/ROAD/117342/2020) Reg. Submission of Hard Copy of Jhansi and Hamirpur Forest Diversion Proposal of Missing Link	

40	26.08.2022	Egis India/LKO/UPCRNDP/2022/1921	EE,PWD,Kanpur	Submission of Micro Plan of Title Holders for Direct Purchase of Land through Mutual Consent for Missing Link (SH-42) under District Jhansi	PWD letter No. 490 Dated 24.08.2022
41	27.08.2022	Egis India/LKO/UPCRNDP/2022/1922	CE,PWD,Lucknow	Hit by Flood due to Heavy Rain and Backflow of Betwa River.	
42	27.08.2022	Egis India/LKO/UPCRNDP/2022/1923	GHV	Site Visit Program of Resident Engineer on 29.08.2022.	
43	29.08.2022	Egis India/LKO/UPCRNDP/2022/1924	CE,PWD,Lucknow	Request to Release of Our Long Pending Payments – <b><u>(Reminder)</u></b>	
44	29.08.2022	Egis India/LKO/UPCRNDP/2022/1925	SE,PWD,Lucknow	Regarding Information about Stolen Road Furniture & Sign Boards	APCO letter No. 774 Dated 25.08.2022
45	29.08.2022	Egis India/LKO/UPCRNDP/2022/1926	APCO	Submission of Final “As Built Drawings” – <b><u>Reminder</u></b>	
46	29.08.2022	Egis India/LKO/UPCRNDP/2022/1927	GAWAR	Submission of Final “As Built Drawings” – Reminder	
47	30.08.2022	Egis India/LKO/UPCRNDP/2022/1928	GHV	Contractor to Submit Draft Contract Addendum/Supplementary Agreement to the Contract for the Granted Extension of Time (EOT) as the Contract Period Extended - <b><u>Reminder</u></b>	
48	30.08.2022	Egis India/LKO/UPCRNDP/2022/1929	NKC	Contractor to Submit Draft Contract Addendum/Supplementary Agreement to the Contract for the Granted Extension of Time (EOT) as the Contract Period Extended - <b><u>Reminder</u></b>	
49	30.08.2022	Egis India/LKO/UPCRNDP/2022/1930	NKC	Submission of Maintenance Programme	
50	30.08.2022	Egis India/LKO/UPCRNDP/2022/1931	GHV-APCO-GAWAR	Submission of Monthly Maintenance Programme as per Contract Agreement	
51	31.08.2022	Egis India/LKO/UPCRNDP/2022/1932	CE,PWD,Lucknow	Photographs of Implementing the Program of Flag Hosting and Planting Trees during the Celebration of Amrit Mahotsav of Independence Day from 11.8.2022 to 17.08.2022	
52	31.08.2022	Egis India/LKO/UPCRNDP/2022/1933	CE,PWD,Lucknow	Hit by Flood due to Heavy Rain and Backflow of Betwa River.	

**INCOMING CORRESPONDANCES of TL OFFICE, LUCKNOW for the m/o AUGUST 2022****ENCLOSURE-1**

Sl. No.	Letter Date	Letter Reference No.	From	Subject	OutGoing Letter Reference
1	02.08.2022	635/UPCRNDP (SH-51)	EE,PWD,Moradabad	Regarding Cleaning of Bushes on both sides of Project Road of SH-51	
2	03.08.2022	703 16C(I)-WBPC/2022	SE,PWD,Kanpur	Regarding Site Inspection and Immediate Remedial Action Required on UPG-01 and UPG-02 project roads by the Authority Engineer during Monsoon Period	
3	04.08.2022	582/800-23/UPCRNDP/WBYC/22	SE,PWD,Lucknow	Principal Secretary Site Visit regarding Tree Plantation on Gola-Shahjahanpur Road (SH-93)	
4	05.08.2022	316/A-5	EE,PWD,Kanpur	EE,Betwa Canal, Jhansi letter No. S-92/Jhs.Pra./841 Dated 28.07.2022 regarding Reinstatement of the Excavated Section of the Garautha-Chirgaon Road from Ch 139+655 to Ch 139+717 for the Irrigation Canal Crossing at Ch 139+686	
5	06.08.2022	721/8C-WBPC/2022	SE,PWD,Kanpur	Progress Review Meeting(Pre Construction Activities of Missing Link) Sheduled at 08.08.2022	E-mail received on 07.08.2022(Sunday) at 4:40PM
6	06.08.2022	645/UPCRNDP	EE,PWD,Moradabad	Draft Copy of As Built Drawings for Structures	E-mail received on 07.08.2022(Sunday) at 4:40PM
7	06.08.2022	650/UPCRNDP	EE,Moradabad	To Construct the Table Top in place of dismantled Speed Bearkers	
8	08.08.2022	NKC/HO/GC/2022-23/191	NKC	Revision in GST Rate from 12% to 18% w.e.f 18.07.2022	

9	08.08.2022	NKC/HO/GC/2022-23/192	NKC	Submission of Maintenance Payment Application No. 07 for the period from 21.03.2022 to 30.06.2022	
10	08.08.2022	NKC/HO/GC/2022-23/193	NKC	Submission of Maintenance Payment Application No. 08 for the period from 01.07.2022 to 31.07.2022	
11	10.08.2022	653/IC	EE,PWD,Moradabad	To Implement the Program of Planting Trees and Flag Hosting during the Celebration of Amarat Mahotsav of Independence Day from 11.08.2022 to 17.08.2022	
12	11.08.2022	603/22008/WBYC/2022	PD,PWD,LUCKNOW	To Implement the Program of Planting Trees during the Celebration of Amarat Mahotsav of Independence Day from 11.8.2022 to 17.08.2022	
13	11.08.2022	734-16 C (i)-WBPC/2022	SE,PWD,Kanpur	Minutes of Meeting (MoM) Dated 08.08.2022 Regarding Review the progress of pre construction Activities (Land Acquisition and Forest Clearance) of Missing Link	
14	16.08.2022	1783/EAP/UPCRNDP/SOCIAL/2022	CE,PWD,Lucknow	Regarding Verification of Affected Gaatas due to Land Acquisition of Bansi-Mehndawal-Khalilabad Road (SH-88)	
15	18.08.2022	612/304/UPCRNDP/WBPC/22	SE,PWD,Lucknow	Regarding Verification of Affected Gaatas due to Land Acquisition of Bansi-Mehndawal-Khalilabad Road (SH-88)	
16	18.08.2022	615/200(2)/UPCRNDP/WBPC/2022	SE,PWD,Lucknow	Land Acquisition of Bahraich-Gonda-Faizabad Road (SH-30)	
17	17.08.2022	739-16 C (i)-WBPC/2022	SE,PWD,Kanpur	Progress Review Meeting of Land Acquisition and Forest Proposal of Missing Link Scheduled to be held on 19.08.2022 at 1:00PM	
18	17.08.2022	740-16 C (I)-WBPC/2022	SE,PWD,Kanpur	Progress Review Meeting of Land Acquisition and Forest Proposal of Missing Link Scheduled to be held on 20.08.2022 at 11:30AM	

19	18.08.2022	APCO/WB-UPPWD/EGIS/ST/773	APCO	Regarding Submission of Maintenance Programme for the m/o August 2022	
20	22.08.2022	745/8C-WBPCK/2022	SE,PWD,Kanpur	Regarding Minutes of Meeting (MoM) Dated 20.08.2022 regarding Pre-Construction Activities of Missing Link	
21	22.08.2022	484/A-6	EE,PWD,Kanpur	Regarding Submission of Microplan and all the Essential Documents required for Registration Individually for each PAP	
22	22.08.2022	1813/1-12/UPCRNDP/CEEAP/2022	CE,PWD,Lucknow	Review Meeting on 02.09.2022 at 11:30AM regarding Environmental/Forest Clearances and EIA Status under Phase-II Roads (SH-30. SH-49 & SH-65) and Stage-II Clearance under the Phase-I Road (UPG-03)	
23	23.08.2022	486/A-6	EE,PWD,Kanpur	Regarding Submission of Forest Proposal of Missing Link	
24	24.08.2022	490/A-6	EE,PWD,Kanpur	Submission of Microplan of Title Holders for direct purchase of land through mutual consent for Missing Link (SH-42)	
25	25.08.2022	707/H.K.	EE,PWD,Aligarh	To provide details of Land Owned by the UPPWD under Hamidpur-Kuchchesar Road (SH-100)	
26	25.08.2022	APCO/WB-UPPWD/EGIS/ST/774	APCO	Regarding Information about Stolen Road Furniture & Sign Boards.	
27	27.08.2022	APCO/WB-UPPWD/EGIS/ST/775	APCO	Regarding Submission the Photographs of Flag Hosting and Planting Trees during the celebration of Amarat Mahotsav of Independence Day from 11.08.2022 to 17.08.2022	
28	29.08.2022	519/A-6	EE,PWD,Kanpur	Regarding ID Cards Preparation after Micro Plan Approved - Missing Link	

29	30.08.2022	1878/Meeting/CEEAP/2022	CE,PWD,Lucknow	MoM Dated 29.08.2022 regarding Progress Review Meeting of Phase-II Roads	
30	31.08.2022	NKC/HO/GC/2022-23/001	NKC	Submission of photographs for implementing the program of Flag Hosting and Tree Plantation during the celebration of Amrit Mahotsav of Independence Day from 11.08.2022 to 17.08.2022	
31	31.08.2022	704/SH-49	EE,PWD,Moradabad	Purchase of Land on Moradabad-Haridwar-Dehradoon (SH-49) Phase-II Road	
32	31.08.2022	814/08C-WBPCK/2022	SE,PWD,Kanpur	Progress Review Meeting of land acquisition and forest prposal of Missing Link on 02.09.2022 at 12:30PM	
33	31.08.2022	815/8C-WBPCK/2022	SE,PWD,Kanpur	Meeting Cancelled regarding Progress Review Meeting of land acquisition and forest prposal of Missing Link on 02.09.2022 at 12:30PM	
34	31.08.2022	APCO/WB-UPPWD/EGIS/ST/776	APCO	Regarding Submission Compliance of Resident Engineer & Sr. Bridge Engineer O&M site inspection note dated 01.08.2022	

**Enclosure-2**

# **PMC Organization Chart**

## 1.13 Consultant's Organization Chart

MONTH - AUGUST 2022

